


Jal Sanchay Abhiyan

Delhi Development Authority


BAMNOLI

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II, 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- Pitching-100%,Footpath Repair-50%, Boundary Wall Repair-100% Plaster-100%, Painting-0% Work is held up due to rain

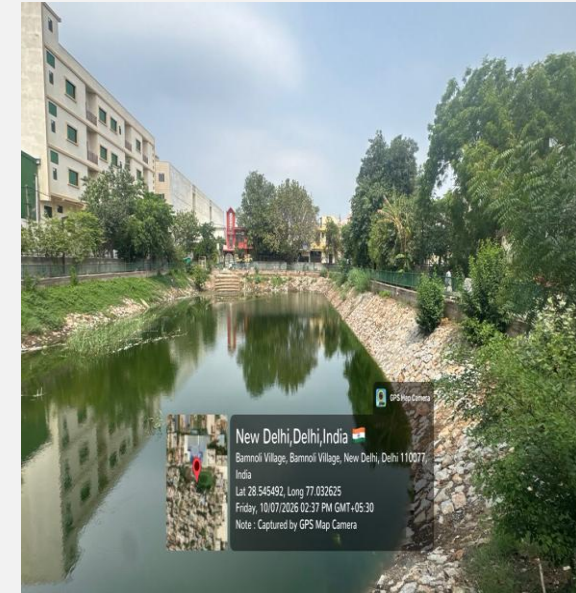


HASANPUR

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II ,8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026

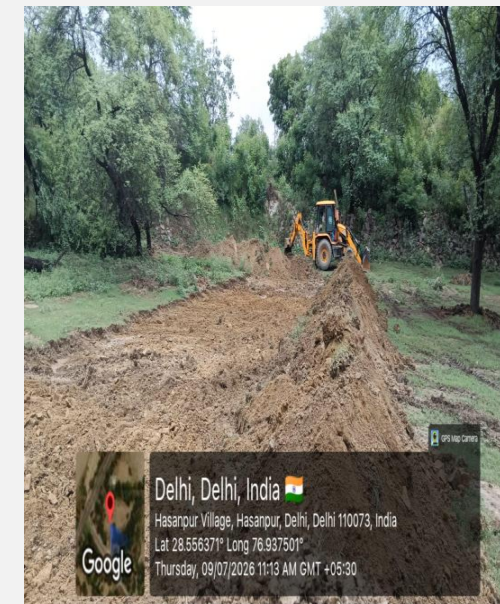

JHARODA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- NIT will be floated by 31.08.2026

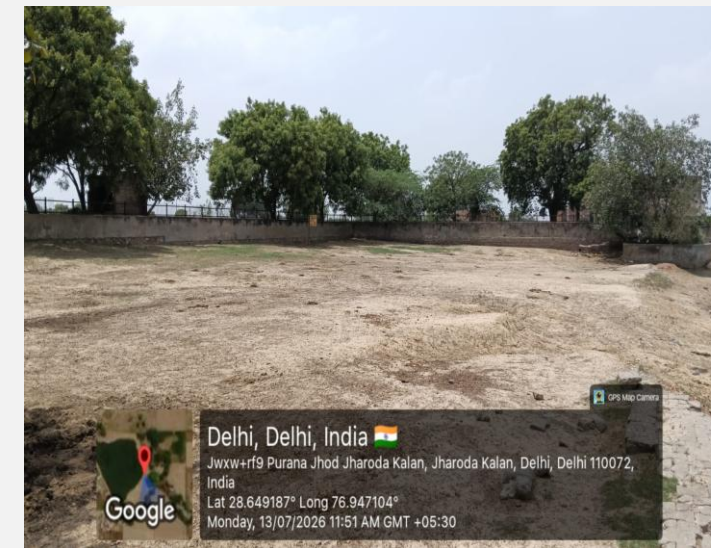


KHAR KHARI RONDH

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026






TIKARI KALAN

- District: West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026

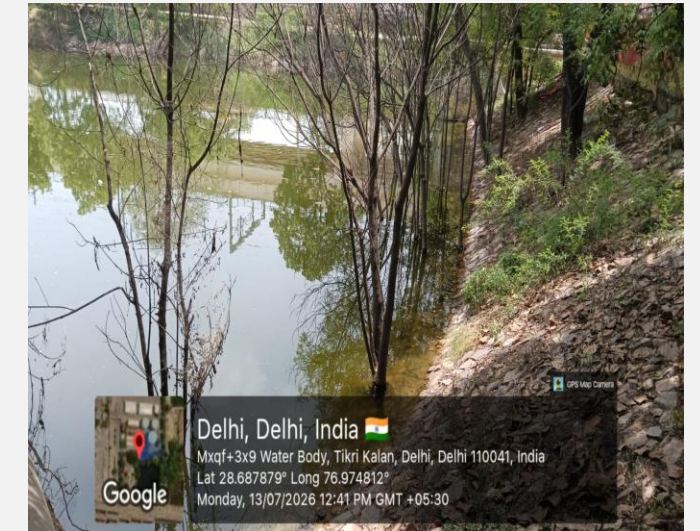

CHAWALA

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026

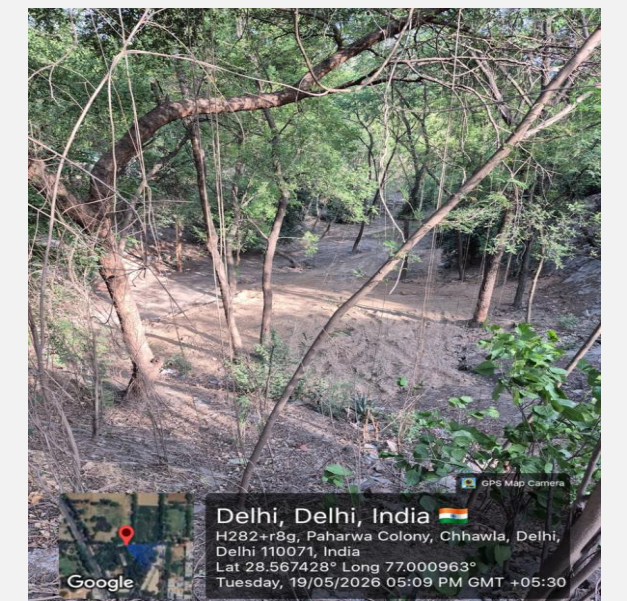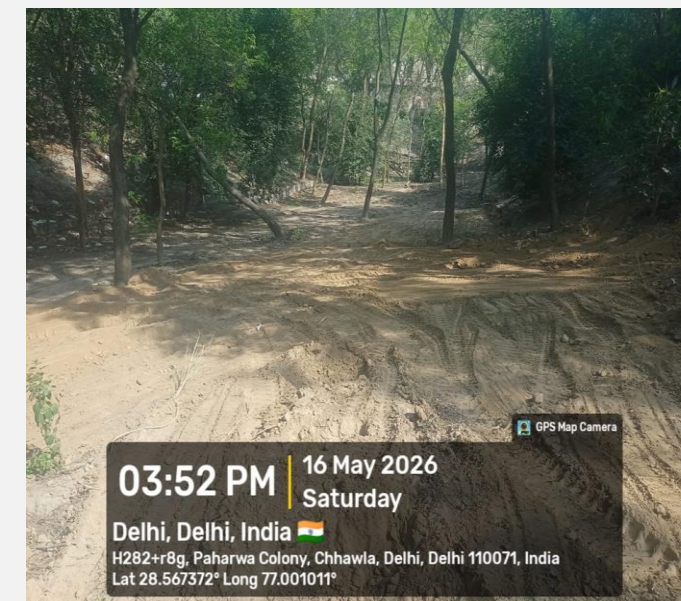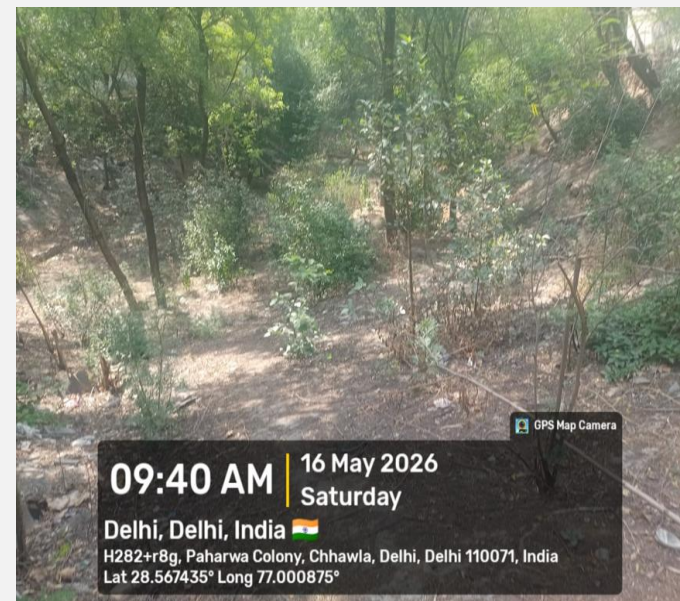

CHAWALA

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026




PINDWALA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- Tender has been called and financial bid will be opened by 30th August, 2026




PINDWALA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026

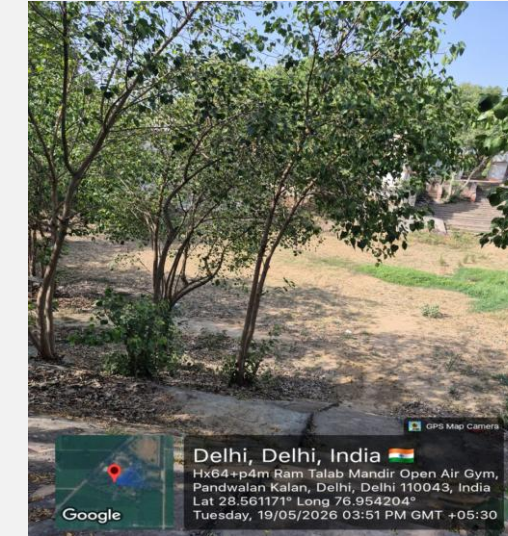

PINDWALA KALAN

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- Tender has been called and financial bid will be opened by 30th August, 2026

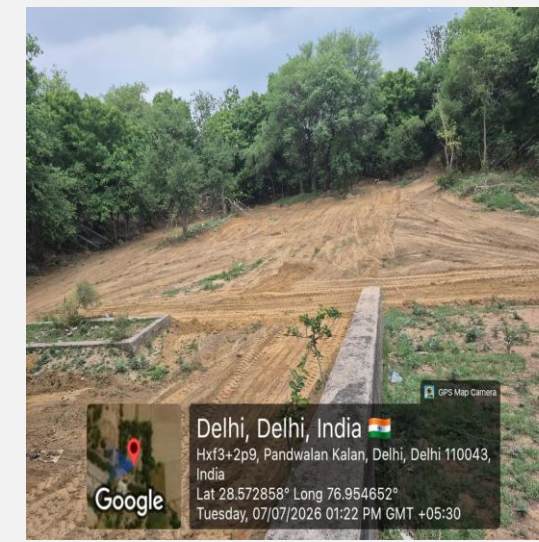


JHUL JHULI

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- Tender has been called and financial bid will be opened by 30th August, 2026





JHUL JHULI

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- Tender has been called and financial bid will be opened by 30th August, 2026

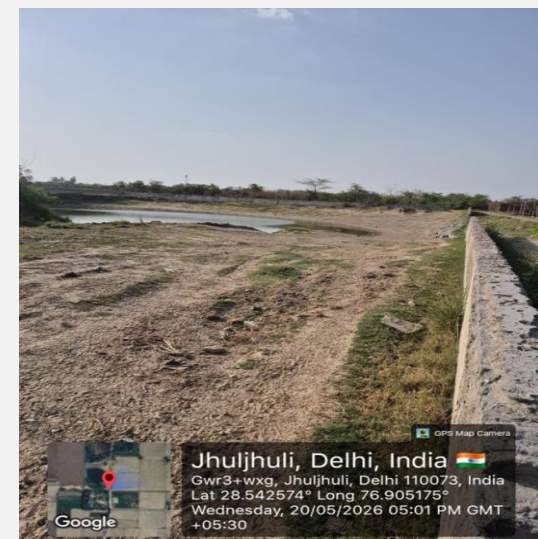



QAJIPUR

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed.
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026

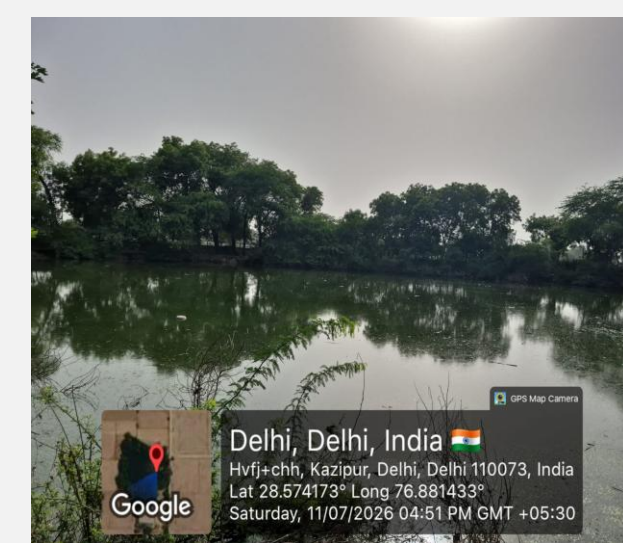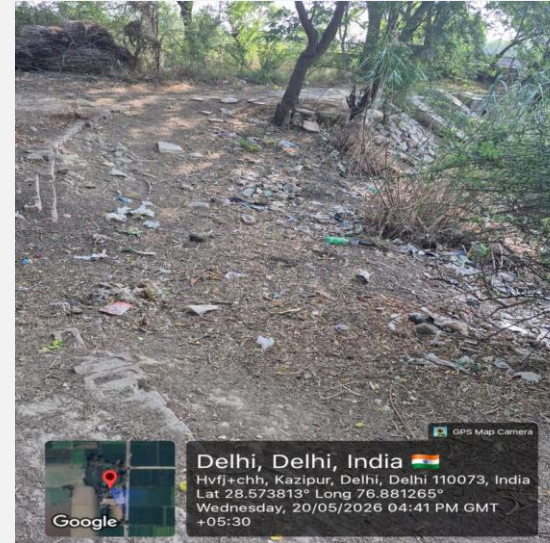


REWLA KHAN PUR

- District: South West
- Concerned Officer: Sh. Rahul Gupta, EE/DMD-II 8755426763
- Phase-I- The work for the cleaning and desilting of phase-I is completed
- Phase-II- PG Letter has been issued to the agency and work will be awarded by 20th August 2026

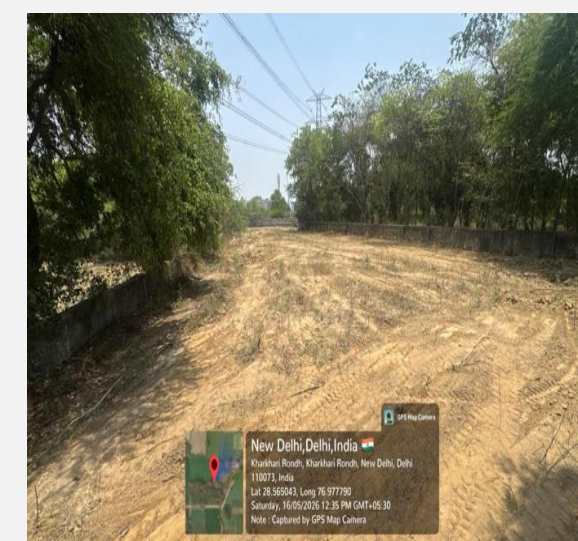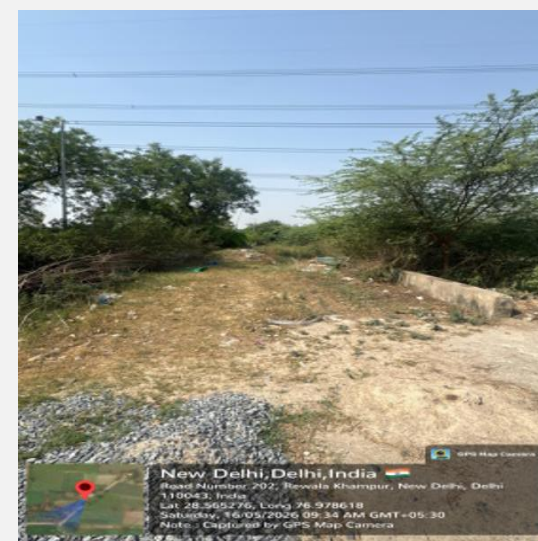




BAPROLA

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated.The Work (Fencing /signage board) will be completed by 31 oct 2026.

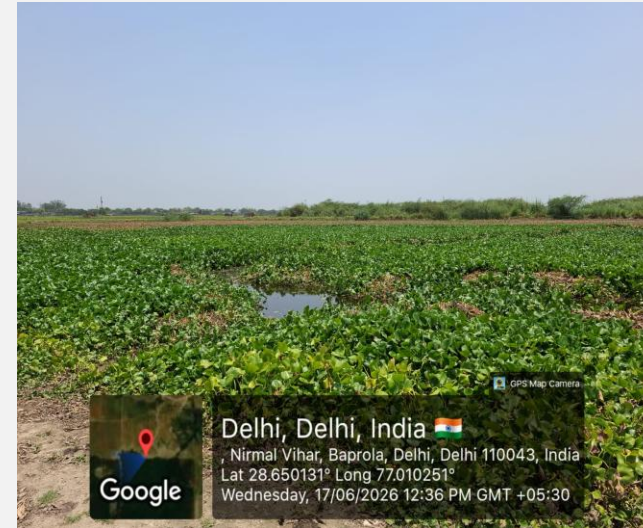


KAMRUDIN NAGAR

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is in progress.
- Phase -2 work :- Tender has been floated.Work (Repair maintenance)will be completed by 31 March 2027

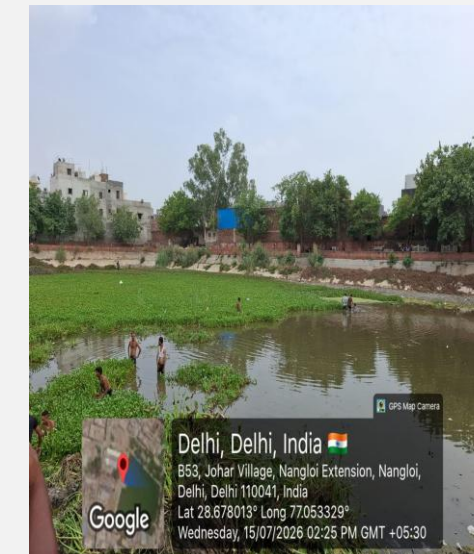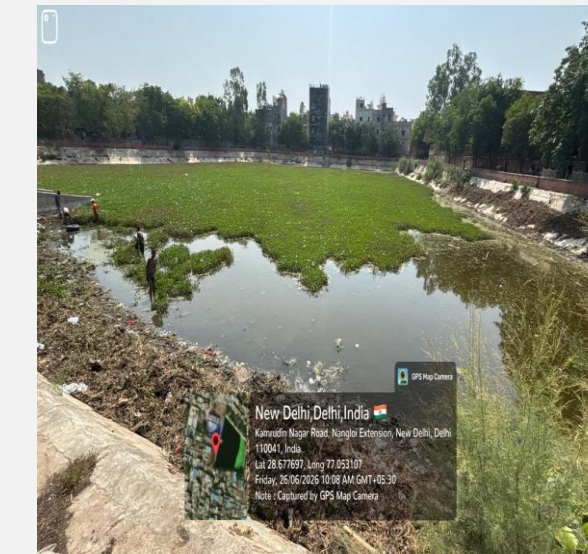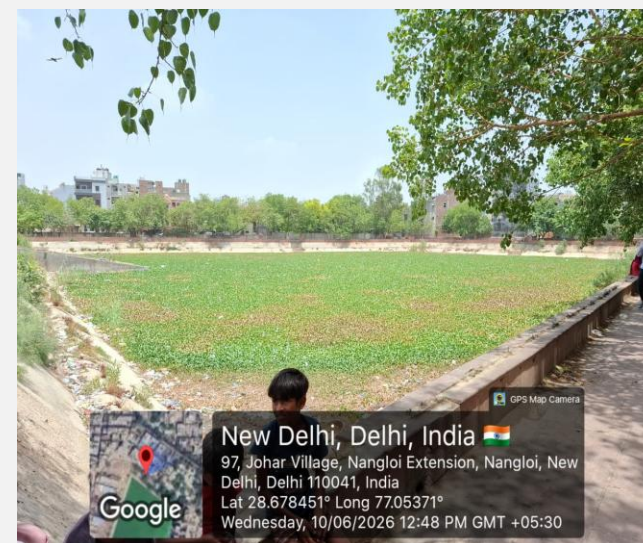


MUNDKA KHASRA NO. 178/1

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated. Work for 2nd phase (Pitching, footpath, Boundary wall etc) will be completed by 31 March 2027

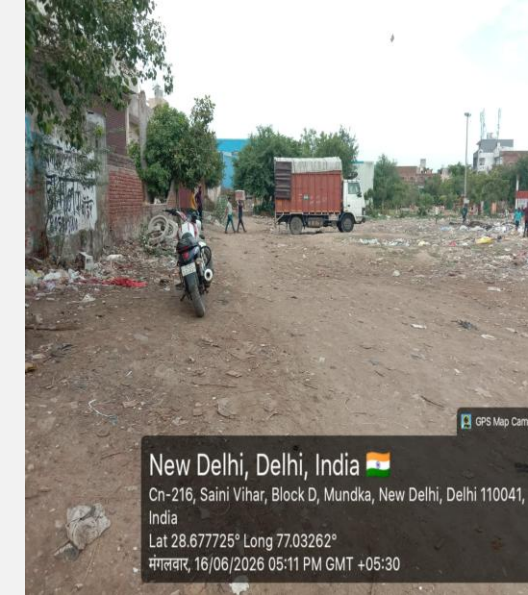

BAKKARWALA KH NO. 83

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Work for 2nd phase (Pitching, footpath, Boundary wall etc) is under tendering process & will be completed by 31 March 2027

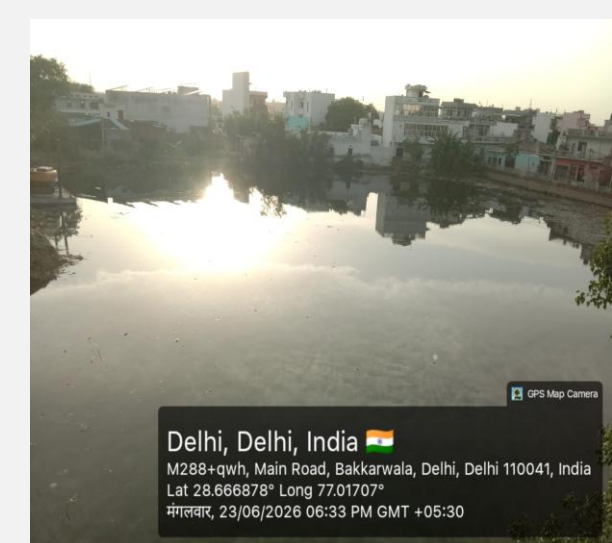



BAKKARWALA KH NO. 82

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated. Work for 2nd phase (Pitching, footpath, Boundary wall etc) will be completed by 31 March 2027





HASTSAL KH. NO. 55/16 & 55/17

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tendering process is in progress. (Pitching, footpath, Boundary wall etc). The timeline for completion of work is 31 March 2027.

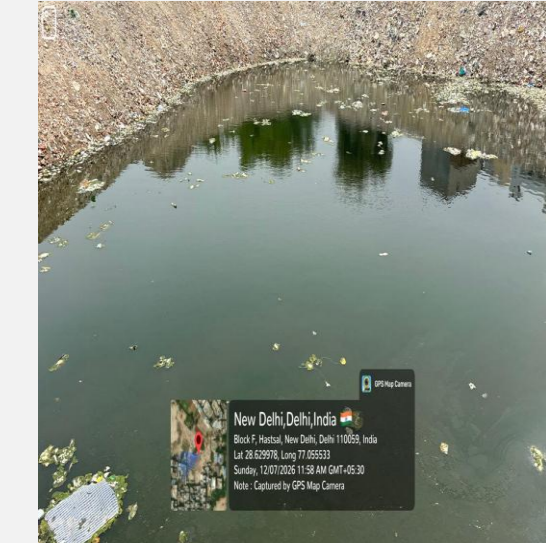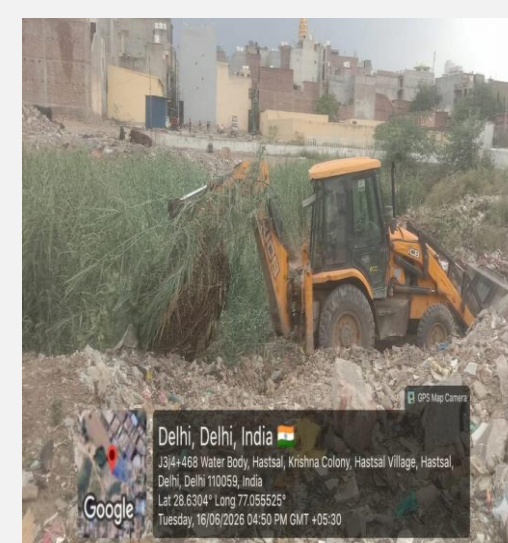



BAPROLA(23//17,23//24,23//25,29//4)

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- Phase-I work is completed.
- Phase-II work :- Tender has been floated.Work (Repair maintenance)will be completed by 31 Dec 2026

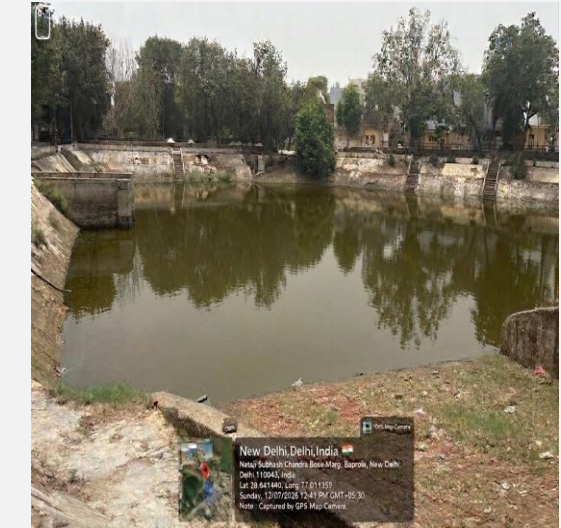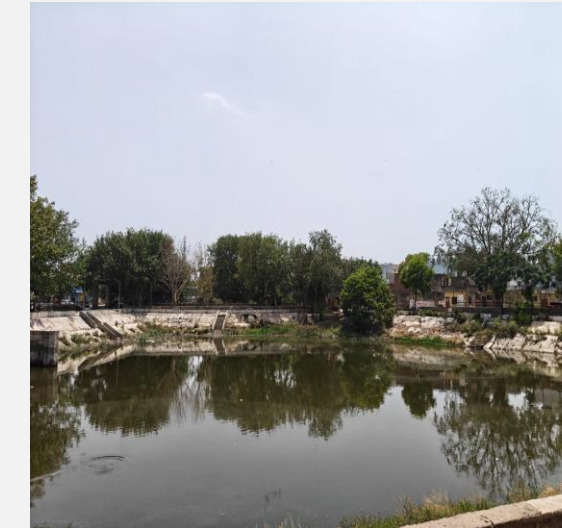

DEENDARPUR(338)/(1087/234)

- District: West
- Concerned Officer: Sh. Nishikesh kumar Mob.8010367794
- Phase-I- During execution, the water body was submerged due to continuous inflow from the PWD drain and rainwater.As MCD drain work is ongoing, the water body is being utilized for wastewater diversion to prevent flooding of nearby areas. Accordingly, the rejuvenation work has been kept in abeyance.
- Phase-II work :- The tender for phase -2 work (Repair and maintenance) work has been uploaded.

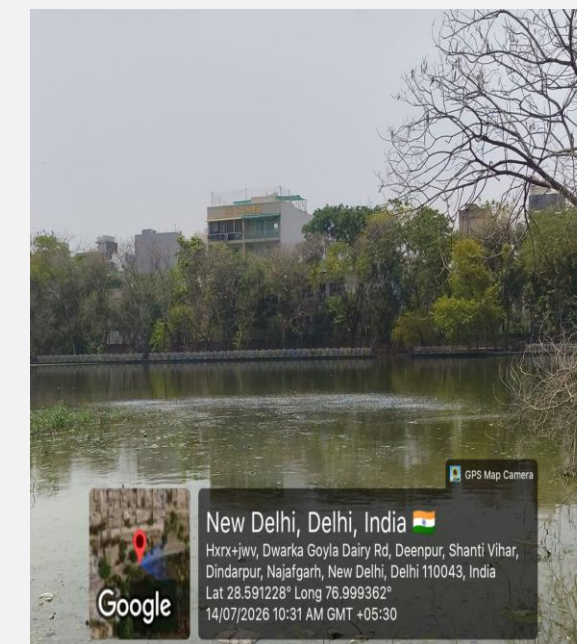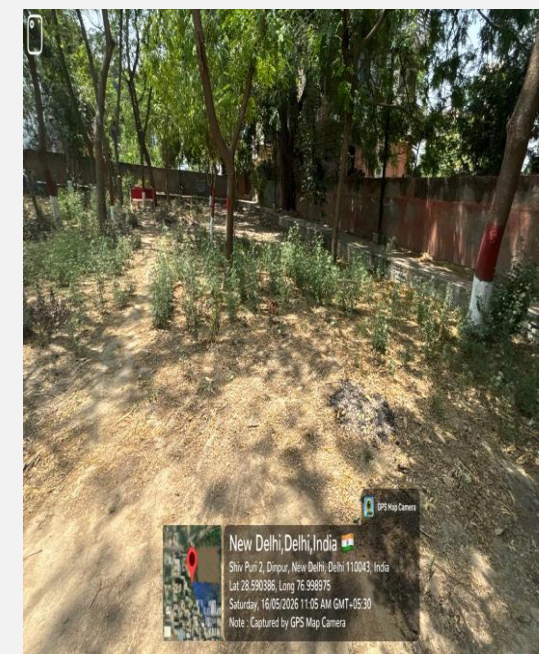



RAJPUR KHURD KH. NO 38

- District: South East
- Concerned Officer: Sh. Sachin kumar(EE)/SMD-5 M-95552 12312
Phase-I- Phase I completed.
- Phase-II- Work for phase 2 started at site. Likely to be completed upto 31.08.2026



MAIDANGARHI KH. NO. 554/2

- District: South
- Concerned Officer: Sh. Sachin kumar(EE)/SMD-5 M-95552 12312
Phase-I- Phase I completed.
- Phase-II- Work for phase 2 started at site. Likely to be completed upto 31.08.2026

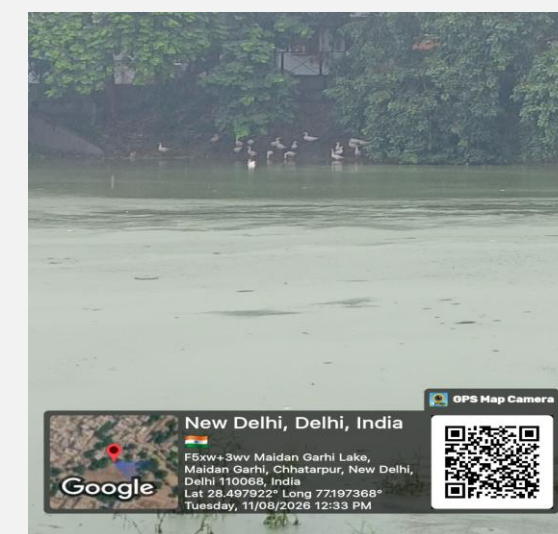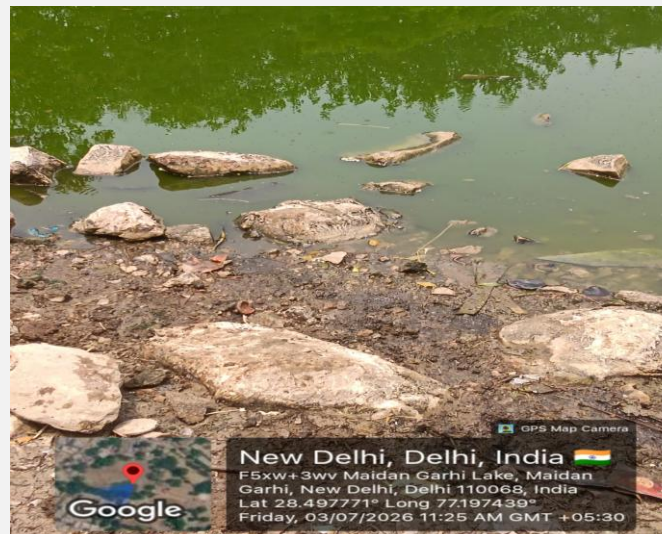


KISHANGARH KH. NO. 1166, 1167, 1168, 109, 1219

- District: South
- Concerned Officer: Sh. Sachin kumar(EE)/SMD-5 M-95552 12312
Phase-I- Phase I completed.
- Phase-II- Work for phase 2 started at site. Likely to be completed upto 31.08.2026




SANJAY LAKE, MAYURVIHAR

- District: East
- Concerned Officer: Sh. Saurabh Mishra EE/HCD-2 M- 7054520525
- Phase-I- Phase I is completed
- Phase-II- Work is under tendering process.

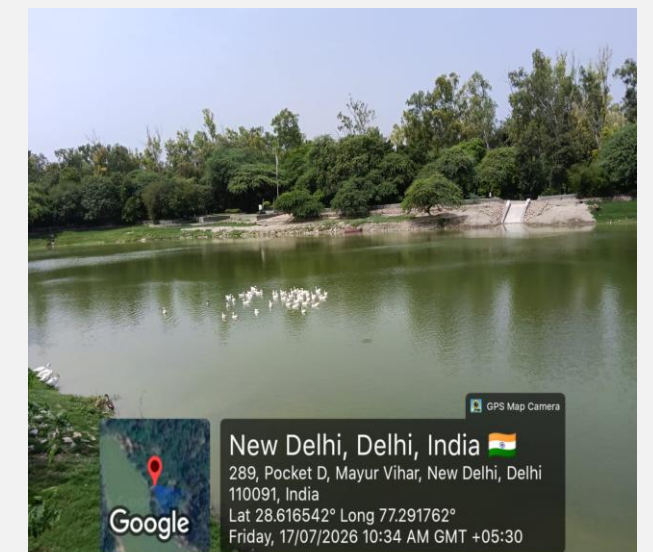


RANGPURI 660(12-12)

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- No Work Required in Phase-II

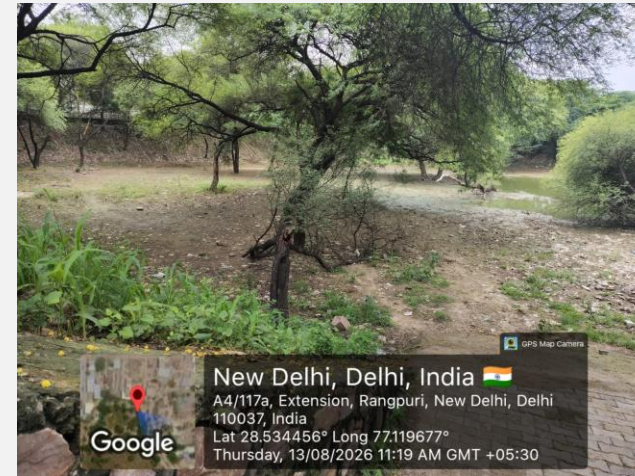

KAPASHERA KH NO. 664/1

- District: South West
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Estimate is under process.the timeline for completion of work is 31.12.2026

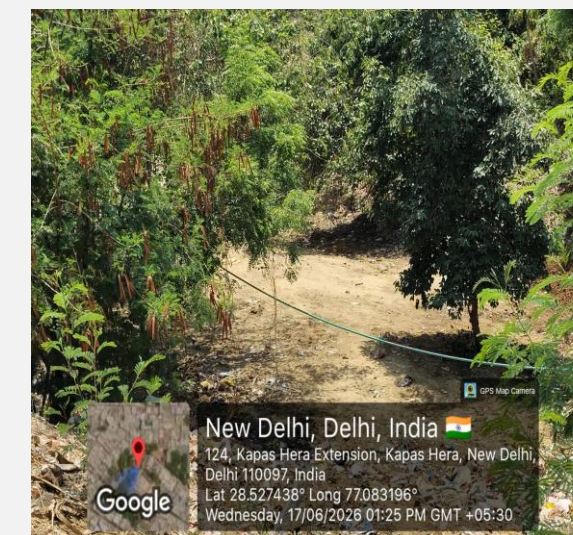



MAHIPAL PUR F/90 KH NO. 1030

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Estimate is under process and the timeline for completion of work is 31.12.2026



RAJOKARI KH NO. 41

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Estimate is under process and the timeline for completion of work is 31.12.2026

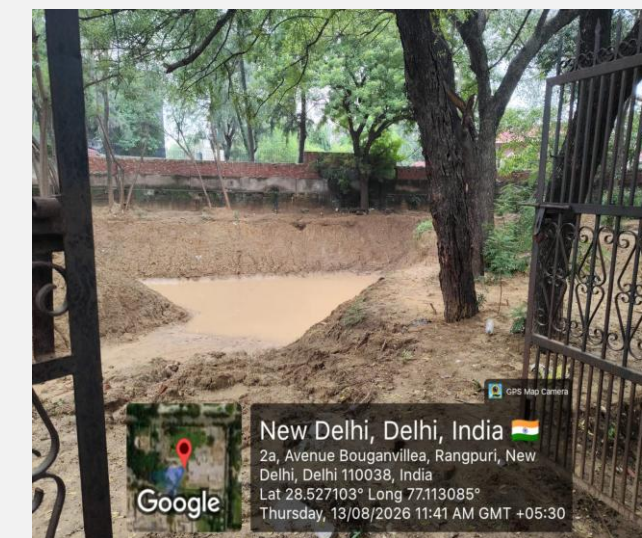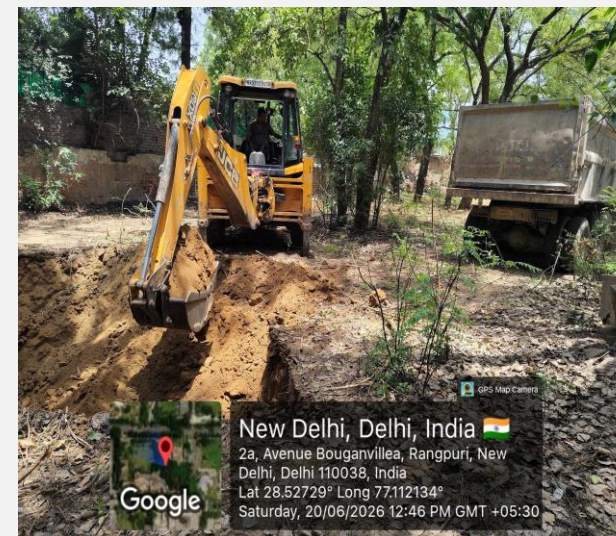

RAJOKARI KH NO. 848

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Estimate is pending zonal office for TS and A/R and M/O and the timeline for completion of work is 31.12.2026



RAJOKARI KH NO. 695

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Estimate is pending zonal office for TS and A/R and M/O and the timeline for completion of work is 31.12.2026



MADANGIR KH. NO. 191-MIN

- District: South
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II- Estimate is pending zonal office for TS and A/R and M/O and the timeline for completion of work is 31.12.2026




GHITORNI 437(17-19)

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II-The A/A and E/S for the 75 KLD STP work is in progress.




RANGPURI 105(6-9)

- District: New Delhi
- Concerned Officer: Sh. Deepak Bhatt(EE) SPD-I M- 98994 62529
- Phase-I- Phase-I work is completed
- Phase-II-The A/A and E/S for the 25 KLD STP work is in progress.

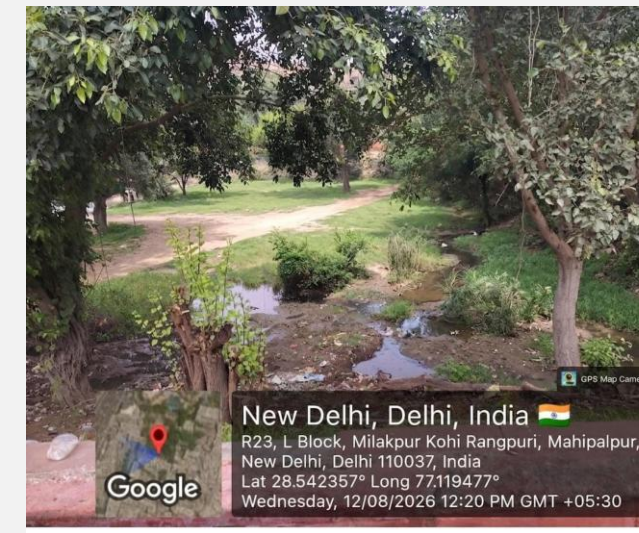


KATEWARA KH. NO. 473, 474, 477, 478, 479, 481

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- completed
- Phase-II- work started w.r.t Construction of Boundary wall, Red sand stone flooring in Steps further Toe wall, Linning, footpath will be completed by 31.12.26.

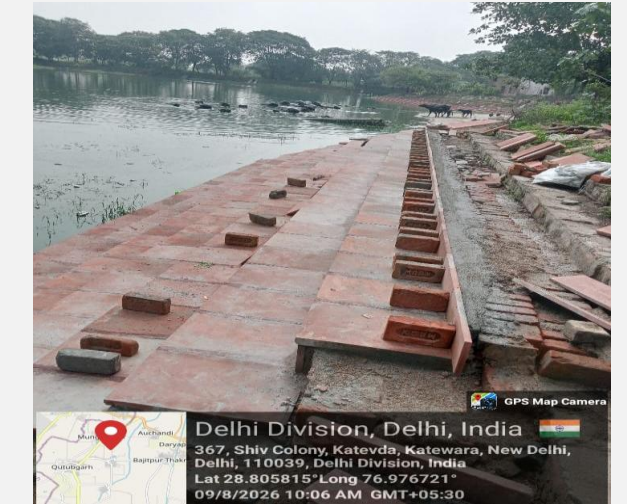



SULTANPUR DABAS KH. NO. 35/37

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 ,9213200667
- Phase-I- work has already been completed
- Phase-II- civil repair work has been started and the same will be completed by 15.10.26.

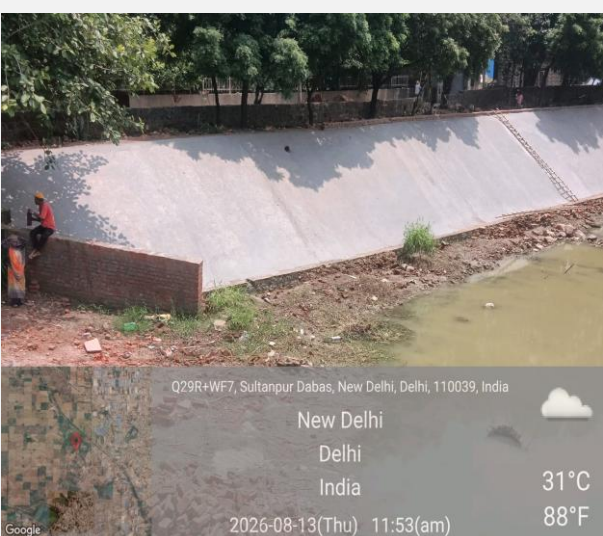




Rani Khera Kh. No. 74/2

- District: Outer North
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3, 9971154443
- Phase-I- Phase -I completed
- Phase-II- Phase -II completed

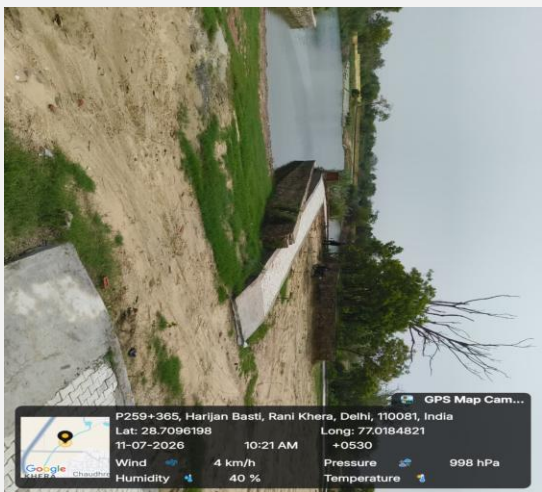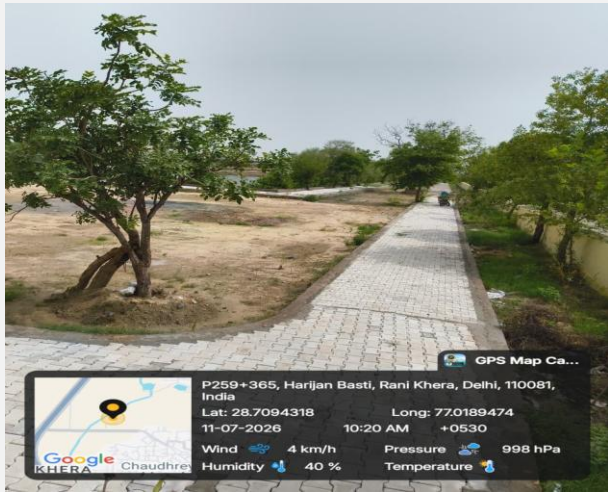


RANI KHERA KH. NO. 9/23 AND 9/17

- District: Outer North
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3 9971154443
- Phase-I- Phase -I completed
- Phase-II- Phase -II completed

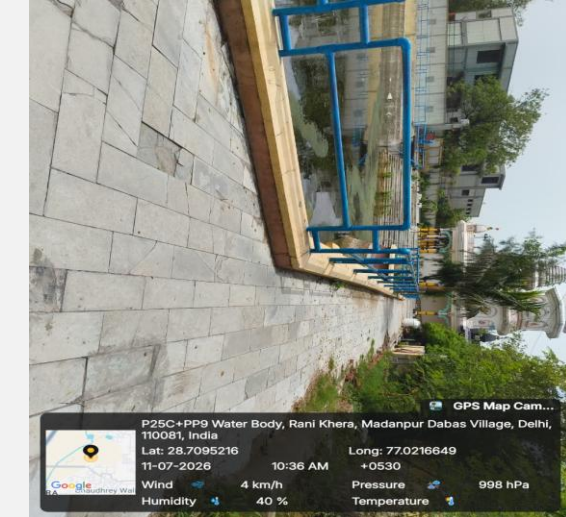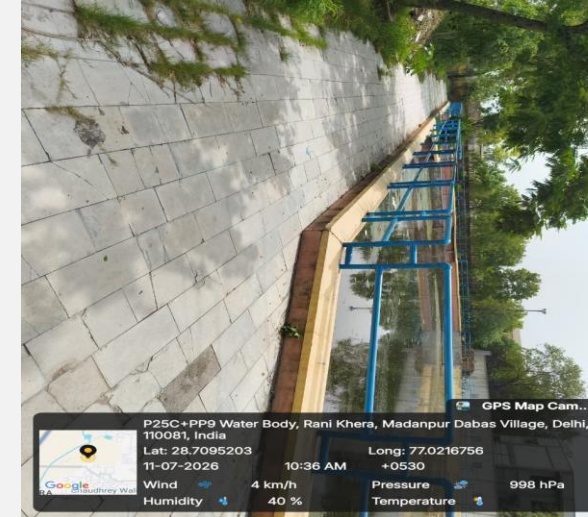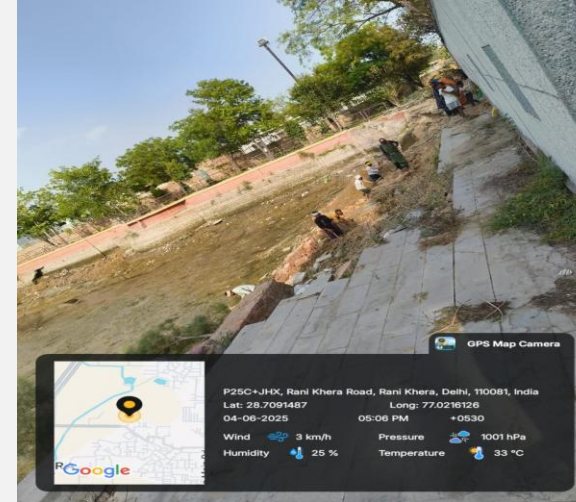

MADANPUR DABAS KH NO. 76

- District: Outer North
- Concerned Officer: Sh.Amit Kumar, EE/RMD-2, M-8178791202
- Phase-I- For Phase-I Cleaning of weeds, scrubs vegetations, Prepration of slope, Jungle cleaning and desilting of water body is completed.
- Phase-II- repair of foothpath, boundary wall and side slopes is under progress and will be completed on 30.09.2026.

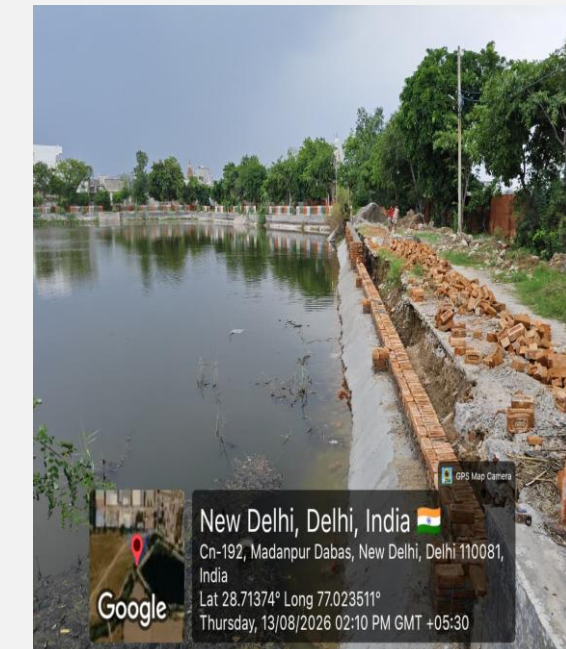

NANGAL THAKRAN KH. NO. 92 MIN

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work is completed
- Phase-II- work started w.r.t Repair of Boundary wall, Red sand stone wall cladding further Toe wall, Linning, footpath will be completed by 31.12.26.



NANGAL THAKRAN KH. NO. 87 MIN

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work is completed
- Phase-II- work started w.r.t construction of Boundary wall, Toe wall, Linning, footpath will be completed by 31.12.26.



CHANDPUR KH. NO. 32/10

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work has been completed
- Phase-II- civil repair work of pitching, boundary wall , footpath work is in progress and dewatering of water body is in progress for lining work and the same will be completed by 20.10.26.



Budhanpur Mazra Kh. No. 36/7, 36/8

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work is completed
- Phase-II- work is in progress and the same will be completed by 20.10.26.




JATKHORE KH. NO. 35/25 MIN

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- Work is completed due time.
- Phase-II- work is in progress and the same will be completed by 30.11.26.




BUDHANPUR MAZRA KHASRA NO 36/10/1

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work Is completed. Civil work will start as soon as the rain intensity will diminish.
- Phase-II- work is in progress and the same will be completed by 31.10.26

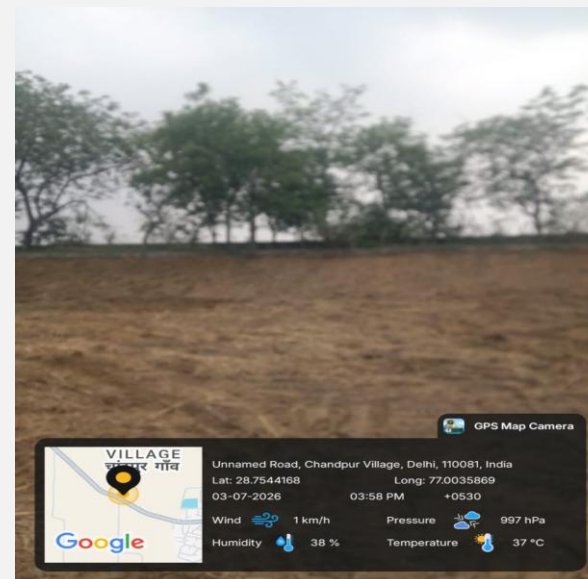

BAWANA KHASRA NO 108/25

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work Is completed.
- Phase-II- work started w.r.t construction of Boundary wall, Toe wall, Linning, footpath will be completed by 31.12.26.

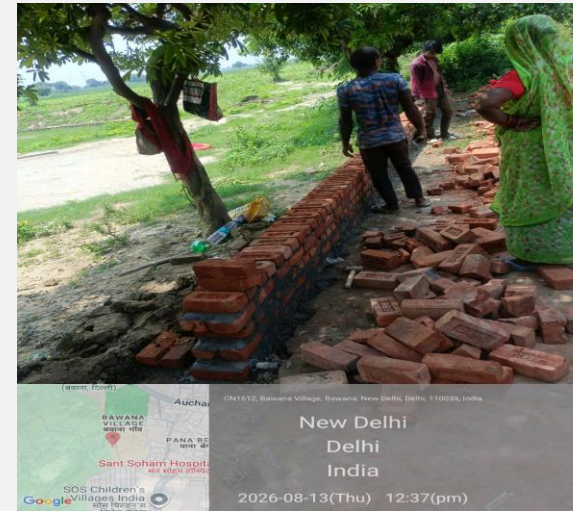

KATEWARA KH NO 824

- District: Outer North
- Concerned Officer: Sh Vijay Sukeriya EE/RMD-8 M -9213200667
- Phase-I- work Is completed.
- Phase-II- work started w.r.t construction of Boundary wall, Toe wall, Linning, footpath will be completed by 31.12.26.



GARHI RANDHALA

- District: North West
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3 9971154443
- Phase-I- The works under Phase-I is completed
- Phase-II- the tender is in progress with a target date of 31.12.2026




GARHI RANDHALA

- District: North West
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3 9971154443
- Phase-I- The works under Phase-I is completed
- Phase-II- the tender is in progress with a target date of 31.12.2026





SAWDA

- District: North-west
- Concerned Officer: Sh. Mohit Parsahr EE/RPD-3
9971154443
- Phase-I- The works under Phase-I is completed.
- Phase-II- Phase II of the work is in progress (total progress 15%) and likely to be completed by 30.10.2026

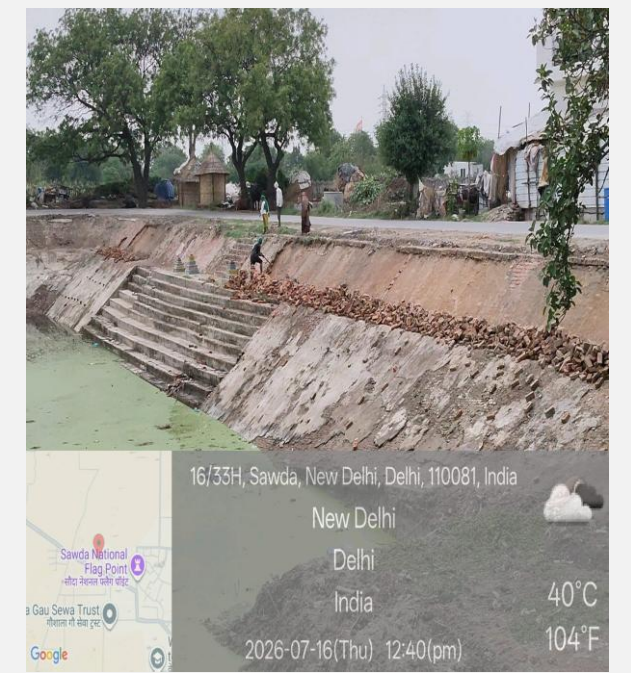


NITHARI

- District: North-west
- Concerned Officer: Sh.Amit Kumar, EE/RMD-2
- Contact No. 8178791202
- Phase-I- For Phase-I Cleaning of weeds, scrubs vegetations, Jungle cleaning and desilting of water body is .
- Phase-II- Work held up due to flooding.

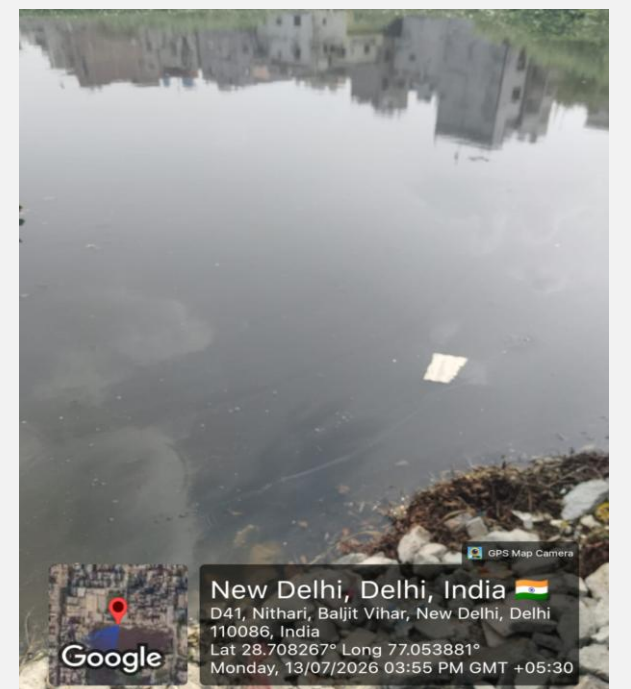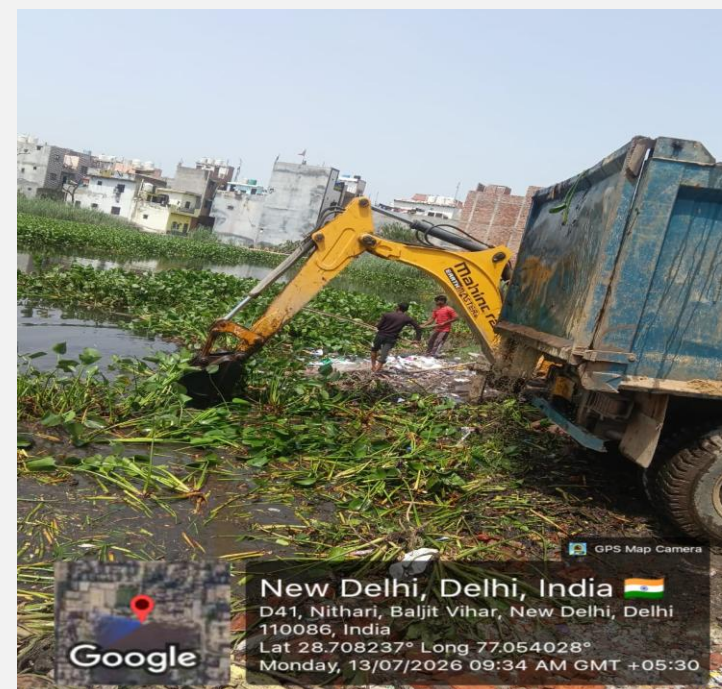

BANKNER

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.

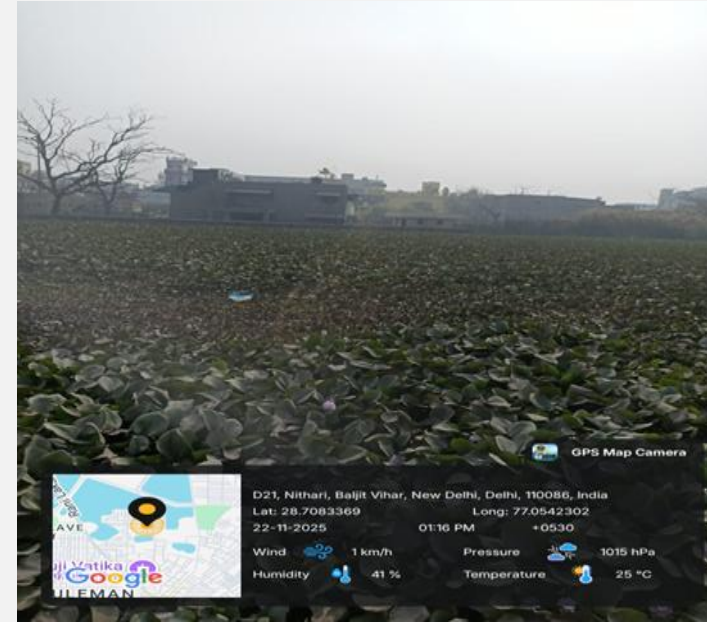

BANKNER

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.



MAMOORPUR

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.




TIKRI KHURD

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.




TIKRI KHURD

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.

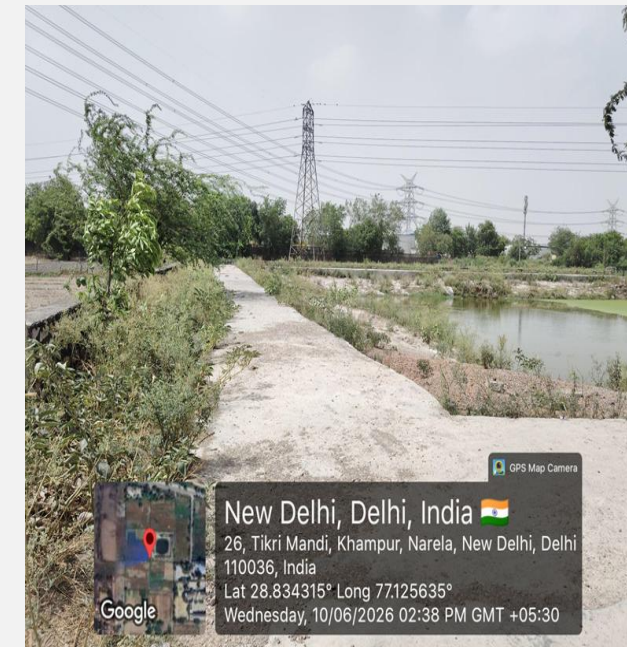



LAM PUR

- District: OUTER NORTH
- Concerned Officer SH GAURAV MEENA (9310334108)
- Phase-I- Phase-I is completed.
- Phase-II- Phase II (slope pitching and fencing etc.) works are under progress.

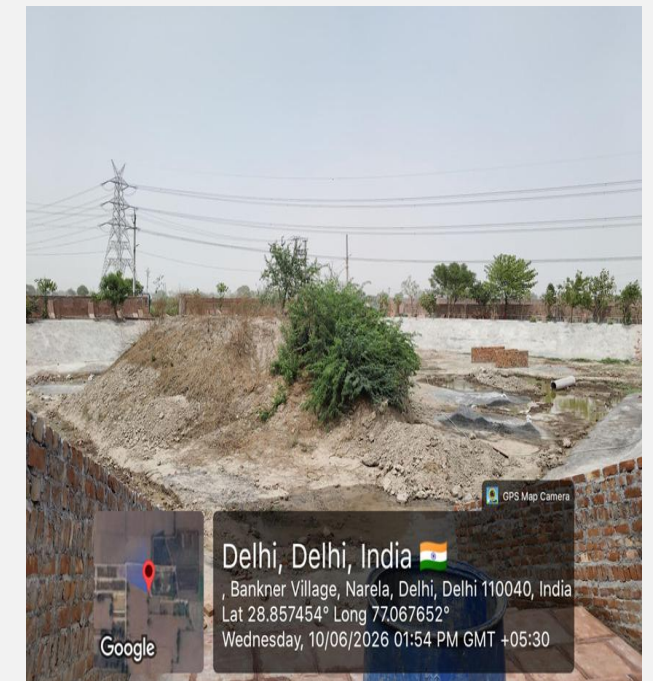

AKBARPUR MAJRA

- District: North West
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I has been Completed
- Phase-II- The work is in progress

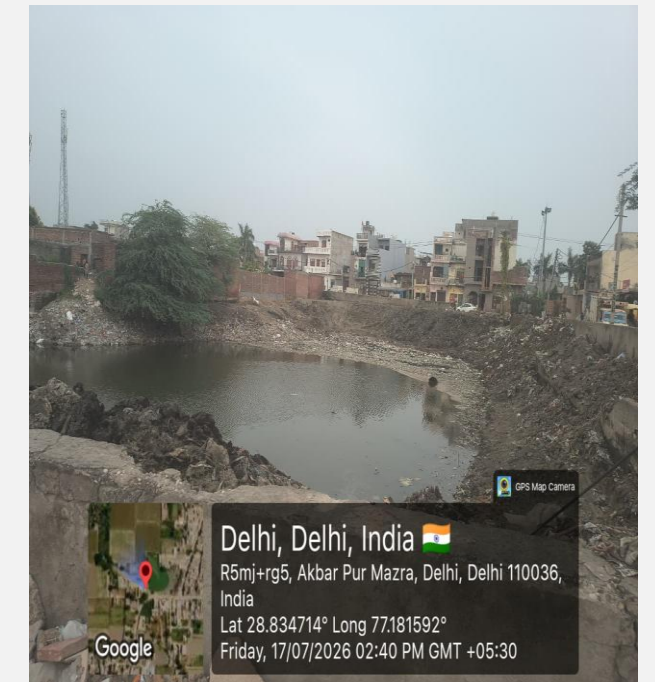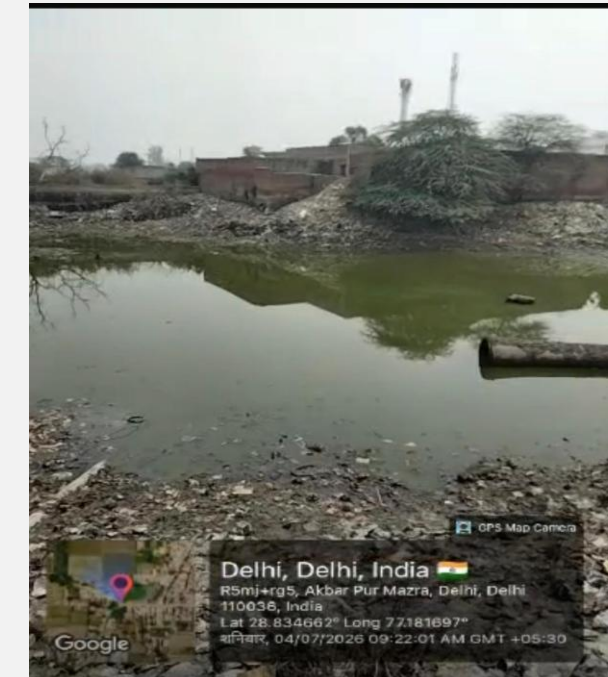

ALIPUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The phase I has been started
- Phase-II- The work is in progress



BAKHTAWAR PUR

- District: North
- Concerned Officer Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work of Phase -I is completed
- Phase-II- The work of phase II is in progress




BAKHTAWAR PUR

- District: : North
- Concerned Officer Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I is in progress
- Phase-II- The work of phase II is in progress




BUDHPUR BIZAPUR

- District: North
- Concerned Officer Sh. Deepak Kumar Sinha(EE)
- Phase-I- The work for Phase-I started and will be complete by 30.08.2026
- Phase-II- Work is in progress

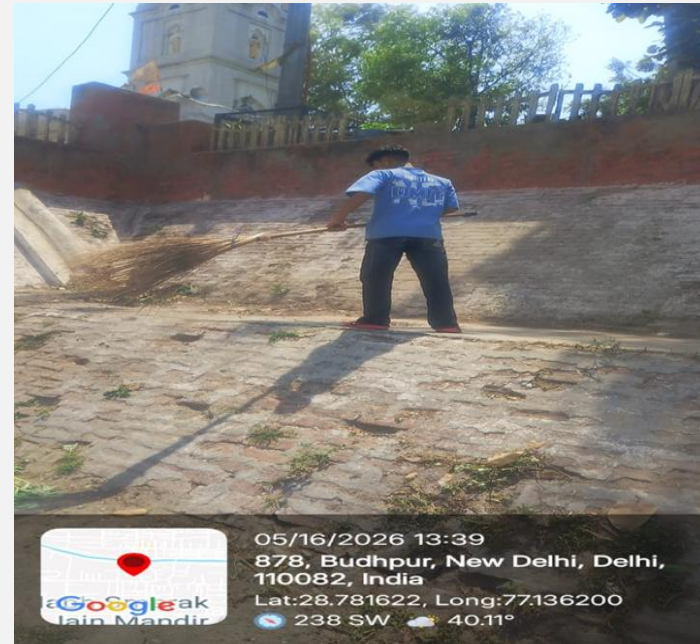


HIRANKI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I is in progress
- Phase-II- Work is in progress

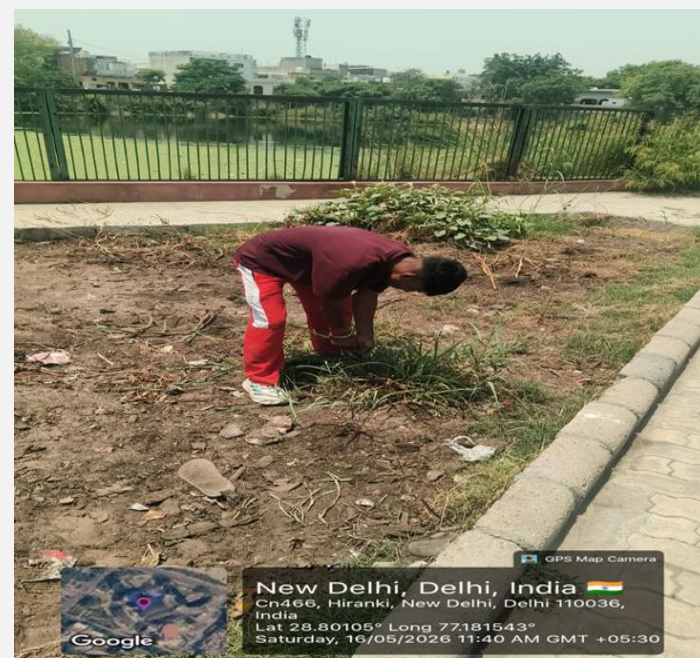

HIRANKI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- The work of Phase -I has been completed
- Phase-II- phase 2 is in progress

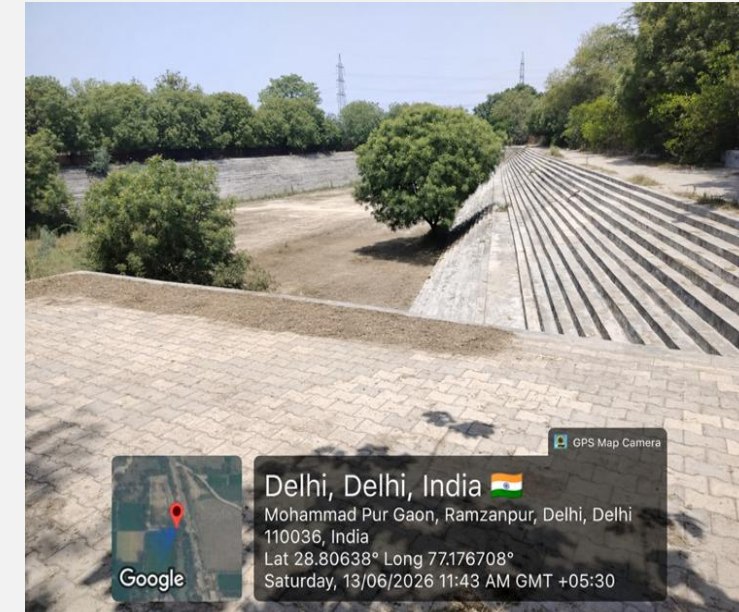

IBRAHIMPUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I is in progress
- Phase-II- phase 2 is in progress



KHERA KALAN

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
Phase-I- The work for Phase-I has been started
- Phase-II- Work is in progress




NANGLI PUNA

- District: North West
- Concerned Officer: Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- The work for Phase-I is in progress
- Phase-II- Work is in progress




SAMAY PUR F/90

- District: Central
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
Phase-I- The work for Phase-I is in progress.
- Phase-II- Work is in progress

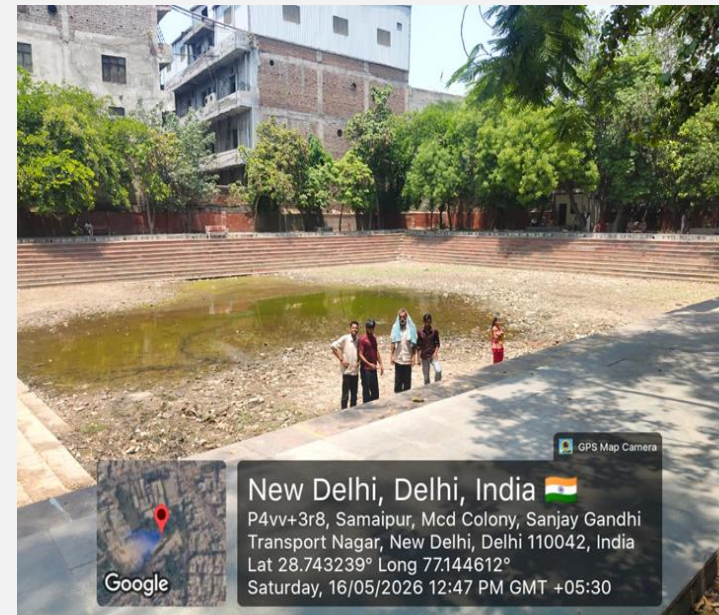


SIRASPUR

- District: Central
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
Phase-I- The work for Phase-I has been Completed
- Phase-II- Work is in progress

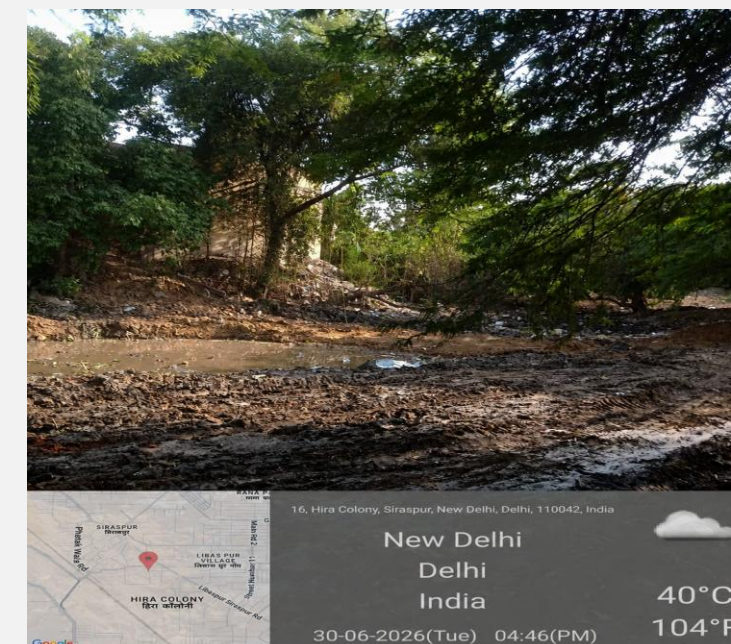


TIGI PUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- Work has been completed for Phase- I
- Phase-II- Work has been completed for Phase-2.

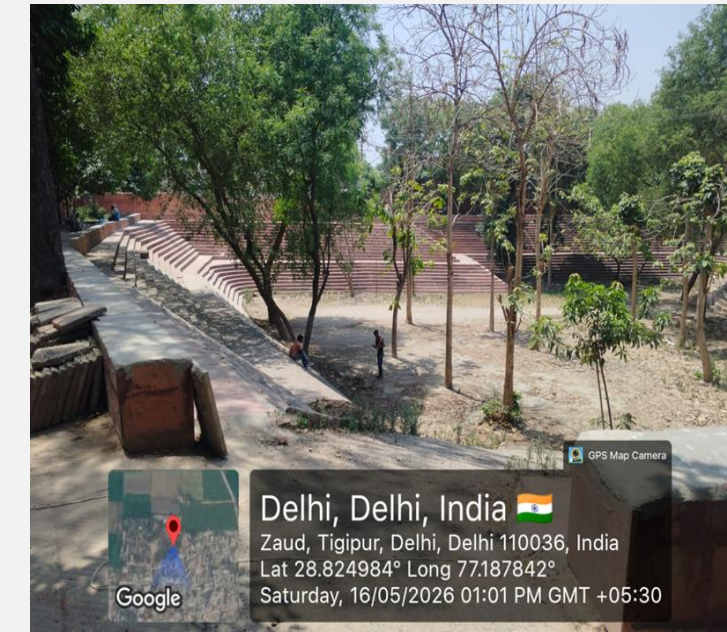

SAHIPUR

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase- I is in progress
- Phase-II- Next week vacant land will be handed over to Horticulture wing for Landscaping

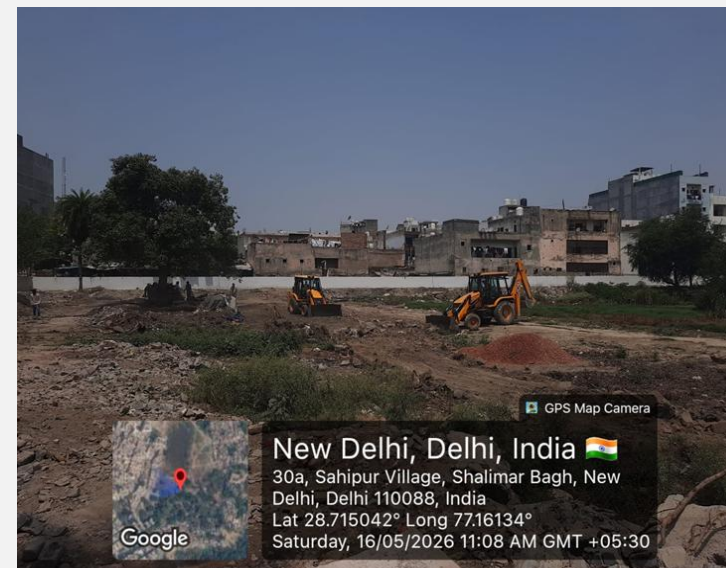

BURARI (4) AND KAMAL PUR MAJRA BURARI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I has been Completed
- Phase-II- phase 2 is in progress



BURARI (4) AND KAMAL PUR MAJRA BURARI

- District : North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE) (8882059444)
- Phase-I- The work for Phase-I is in progress
- Phase-II- phase 2 is in progress



BURARI (4) AND KAMAL PUR MAJRA BURARI

- District: North
- Concerned Officer: Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- The work for Phase-I in tendering process.
- Phase-II- Tender at acceptance stage



BURARI (4) AND KAMAL PUR MAJRA BURARI

- District: Central
- Concerned Officer: : Sh. Deepak Kumar Sinha(EE (8882059444)
- Phase-I- The work for Phase-I is in progress
- Phase-II- phase 2 is in progress






BAKHTAWAR PUR

- District: North
- Concerned Officer Sh. Deepak Kumar Sinha(EE) (8882059444)
Phase-I- The work for Phase-I is completed
- Phase-II- phase 2 is in progress





SHAHBAD MOHD.PUR F/03, (NEAR RAILWAY FATAK)

- District: New Delhi
- Concerned Officer: Sh.Vishal Kumawat EE/HCD-7 9759835794
Phase-I- Phase-I work is completed
- Phase-II- Phase -2 work :- Tender was invited for Phase-2.
Financial bid has been opened, PG letter has been issued and the work is likely to be awarded by 20.08.2026

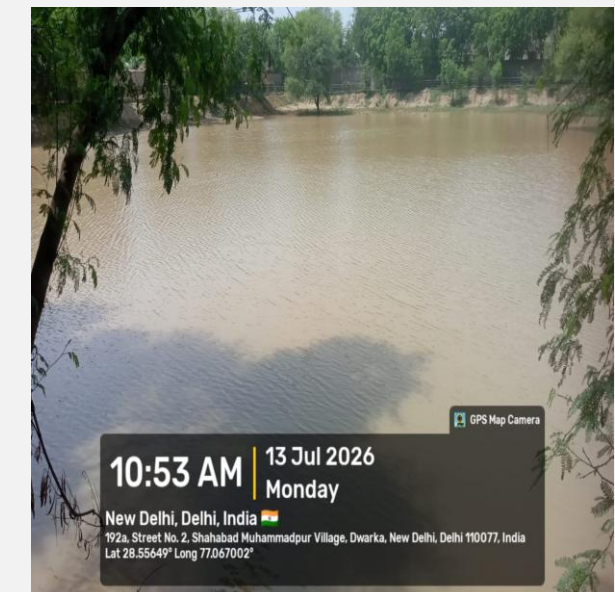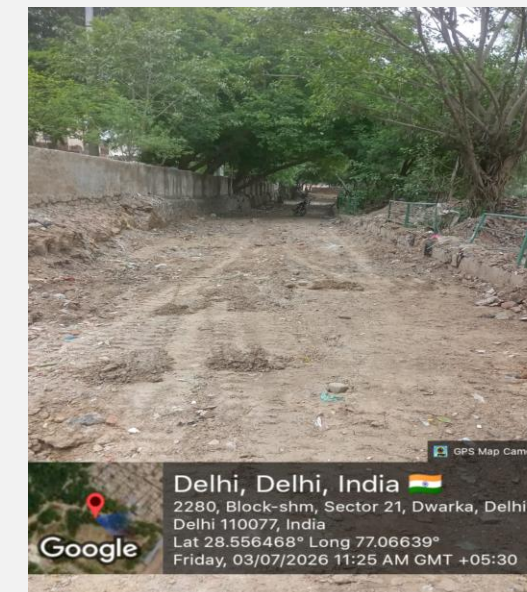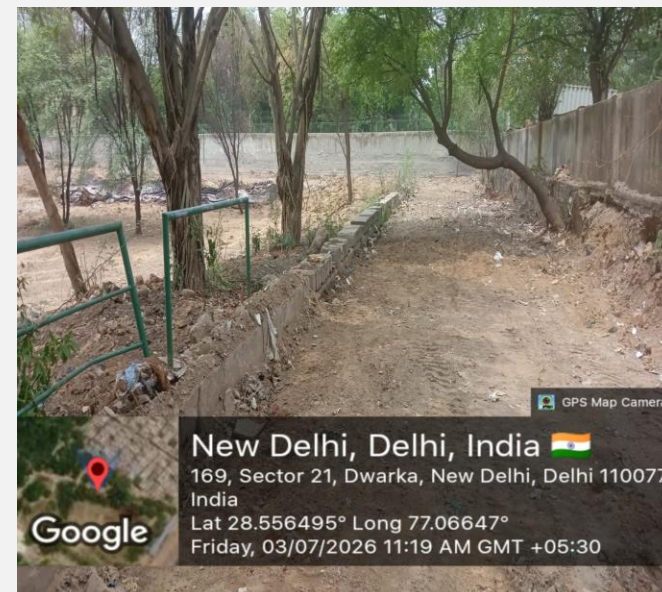




GARHIPEERAN F/89 @ PEERAGARHI (PARK AND LAKE AT DISTRICT PARK, PASCHIM VIHAR)

- District: West
- Concerned Officer : Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Phase-I work is completed.
- Phase-II- Phase -II work such as fencing and already exist at waterbody. However few maintenance works is required such as installation /repar of signage boards, repairing barbed wire fencing, repair of pathway etc. Estimate for overall maintenance of park has been submitted to higher office for scrutiny.

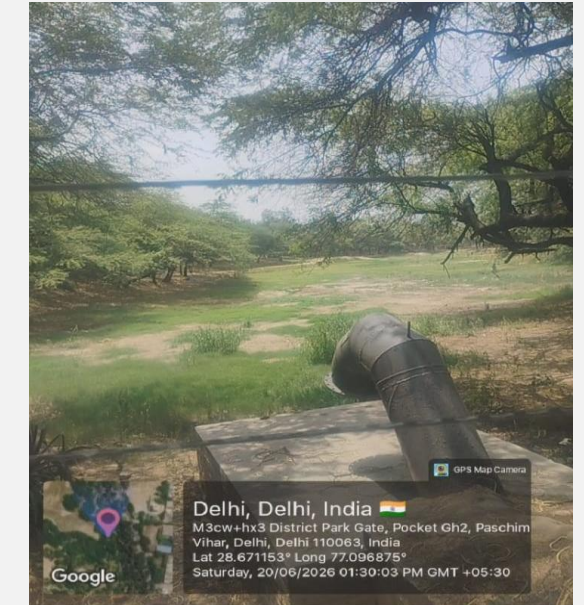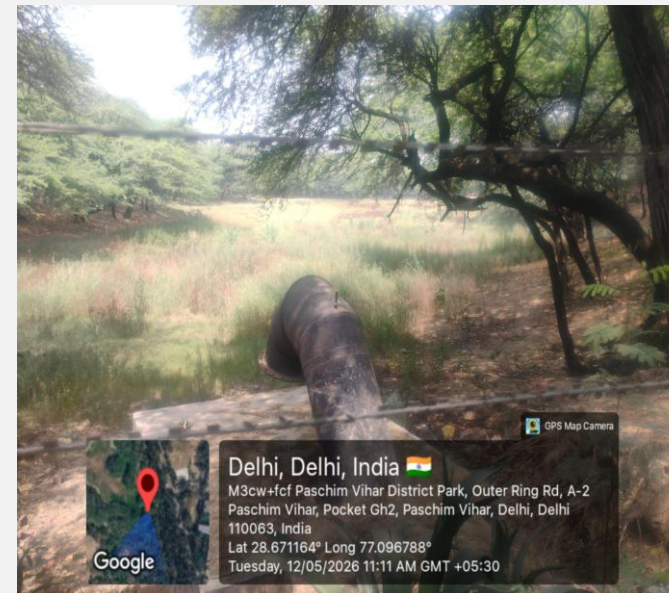

MADIPUR F/74 (PARK AND LAKE AT BHAGWATI TALAB, MADIPUR)

- District: West
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Phase-I work is completed
- Phase-II- Waterbody already has ghats and fencing, however major repair and maintenance is required for the same. Also park is under 30 Model parks scheme and estimate for the same has already been submitted to higher offices.

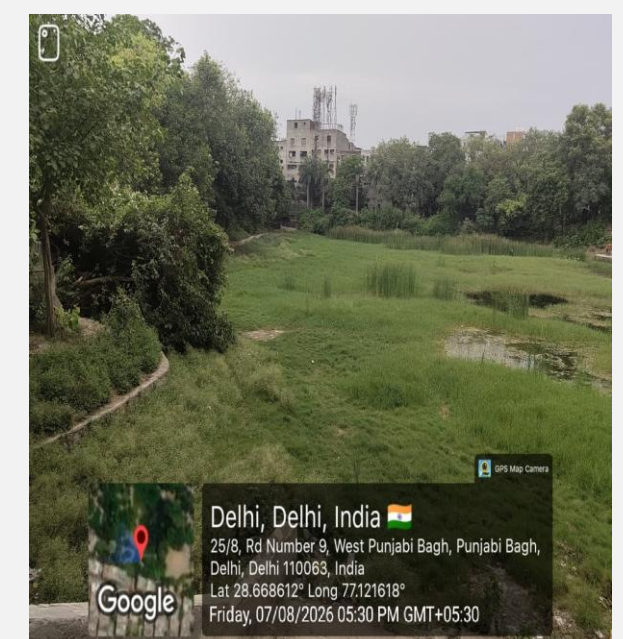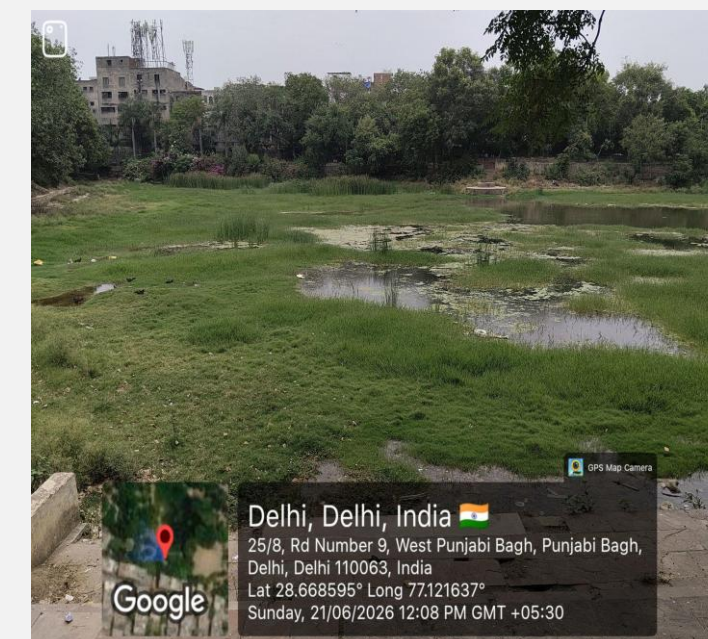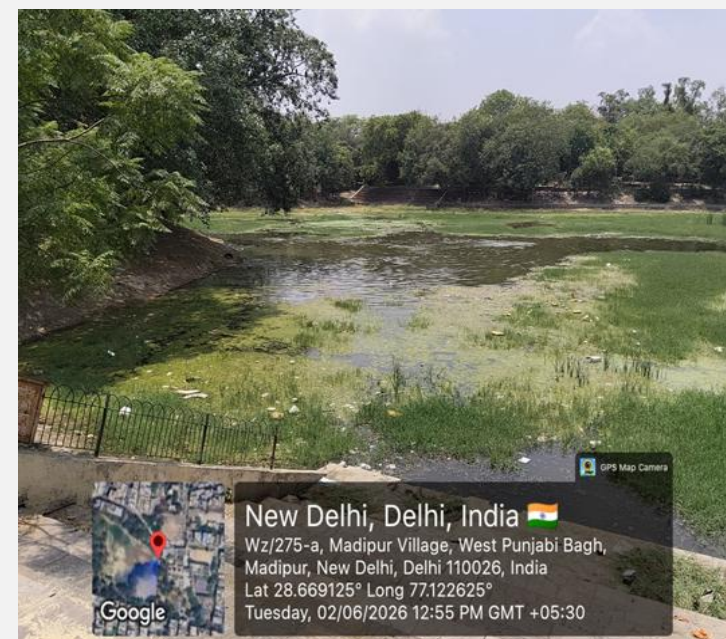

MADIPUR F/75 (PARK AND LAKE AT MADIPUR VILLAGE)

- District: West
- Concerned Officer Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Phase-I work is completed
- Phase-II- Waterbody already has ghats and fencing, however major repair and maintenance is required for the same. Also park is under 30 Model parks scheme and estimate for the same has already been submitted to higher offices.



KILOKARI F/66

- District: South East
- Concerned Officer: Sh. Durga Prasad Chaini 8800432562
- Phase-I- Completed
- Phase-II- Phase-I work has been completed and Phase-II work will be completed by 30.08.2026. Phase-II maintenance work i.e. repair of fencing and pitching work in progress.





KALINDI AVIRAL (AOL) WATER BODY NO.-2, VILLAGE KILOKARI, SOUTH EAST, DELHI

- District: South East
- Concerned Officer: Sh. Durga Prasad Chaini 8800432562
- Phase-I- cleaning work such as weeding out, removal of plastic waste has been completed. The desilting and excavation work in progress. The work will be completed by 31.08.2026..
- Phase-II- Phase -II work such as fencing and already exist at waterbody. However few maintenance works is required such as repainting of signage boards and barbed wire fencing new the damaged portion. the same will be started after completion of phase -I



KALINDI AVIRAL (AOL) WATER BODY NO.-3, VILLAGE KILOKARI, SOUTH EAST, DELHI

- District: South East
- Concerned Officer Sh. Durga Prasad Chaini 8800432562
- Phase-I- cleaning work such as weeding out, removal of plastic waste has been completed. The desilting and excavation work are in-progress. The work will be completed by 31.08.2026.
- Phase-II- Phase -II work such as fencing and already exist at waterbody. However few maintenance works is required such as repainting of signage boards and barbed wire fencing new the damaged portion. the same will be started after completion of phase -I

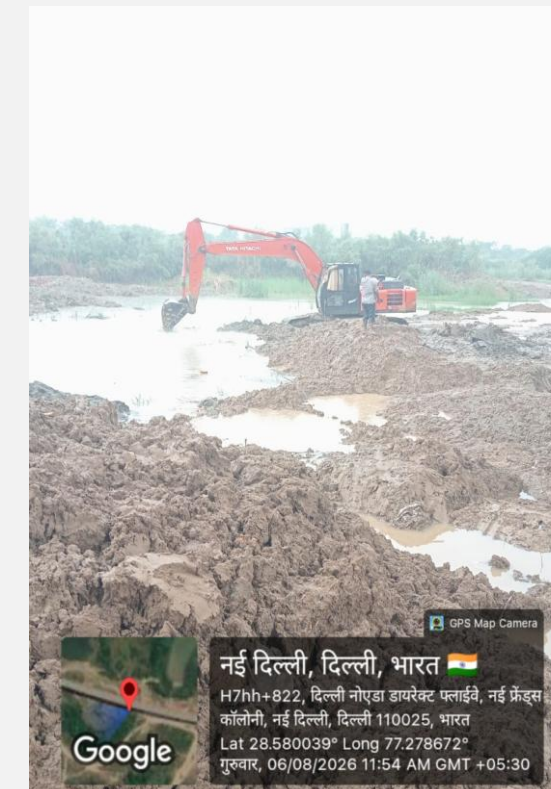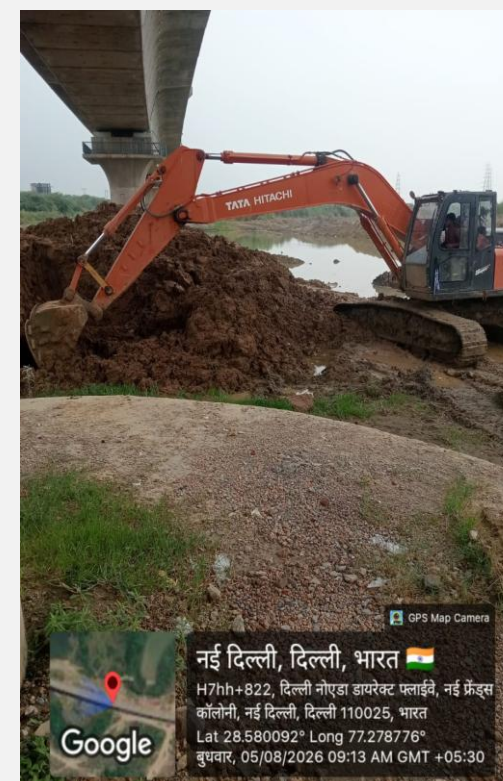




KALINDI AVIRAL (AOL) WATER BODY NO.-4, VILLAGE KILOKARI, SOUTH EAST, DELHI

- District: South East
- Concerned Officer Sh. Durga Prasad Chaini 8800432562
- Phase-I- cleaning work such as weeding out, removal of plastic waste has been completed. The desilting and excavation work are in-progress. The work will be completed by 31.08.2026.
- Phase-II- Phase -II work such as fencing and already exist at waterbody. However few maintenance works is required such as repainting of signage boards and barbed wire fencing new the damaged portion. the same will be started after completion of phase -I



GHONDA GUJRAN KHADDAR

- District: North East
- Concerned Officer Sh. Sandeep Kushwaha EE/HCD-10 9868915016
- Phase-I- Phase-I work is completed.
- Phase-II- The work for Phase-2 is not required.

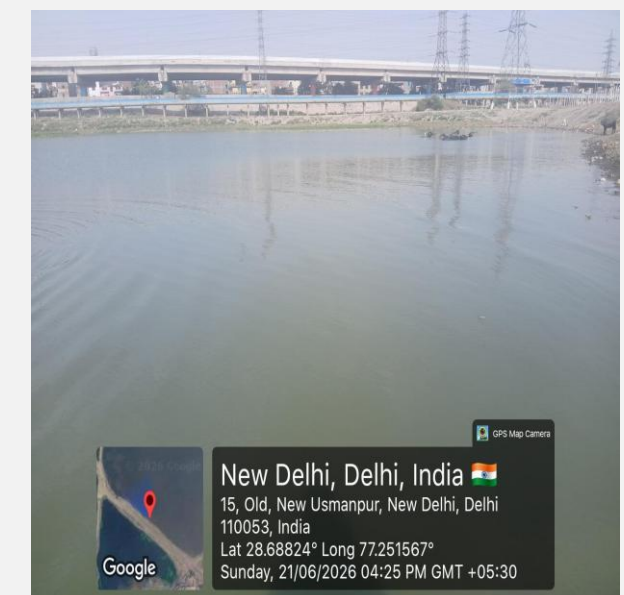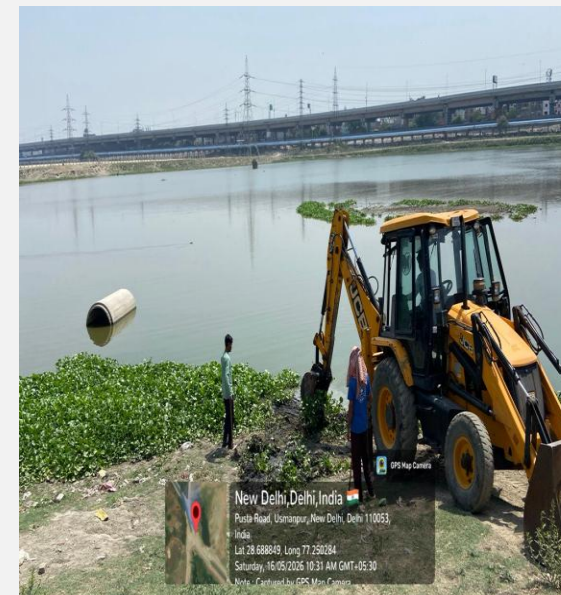



USMANPUR F/89

- District: North East
- Concerned Officer: Sh. Sandeep Kushwaha EE/HCD-10
9868915016
- Phase-I- Phase-I work is completed.
- Phase-II- The work for Phase-2 is not required.



K.N. RIDGE KHUNIJHEEL (SERPENTINE LAKE)

- District: North
- Concerned Officer Sh. Sandeep Kushwaha EE/HCD-10
9868915016
- Phase-I- Phase-I work is completed.
- Phase-II- The work for Phase-2 is not required.

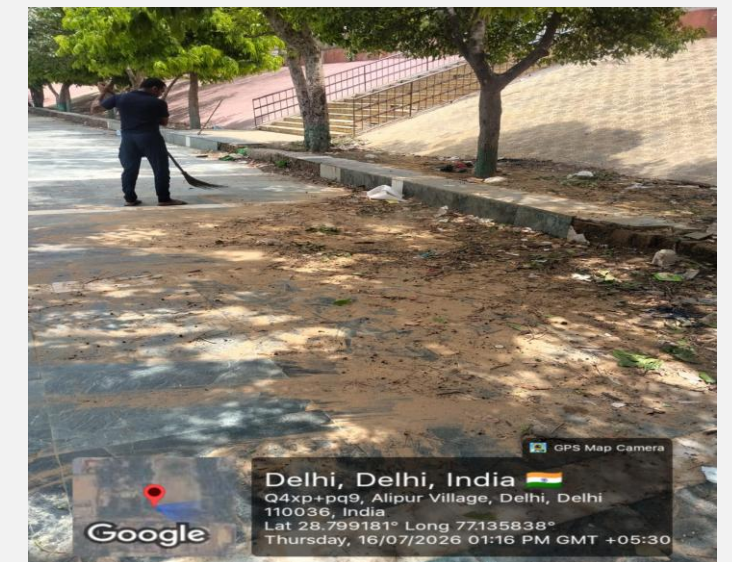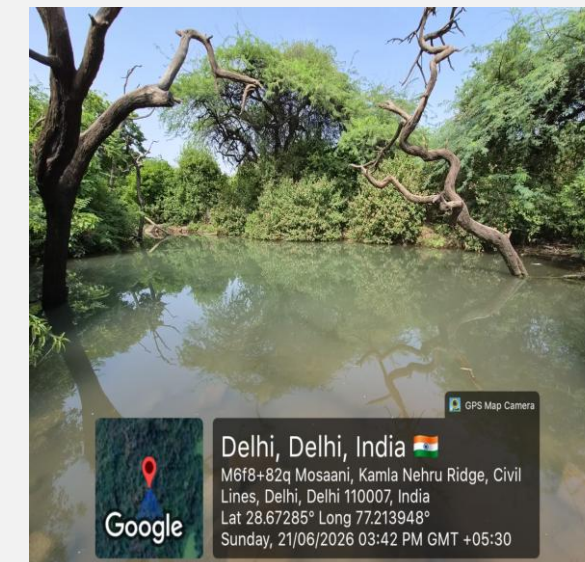



JHARODA MAJRA, BURARI.

- District: North East
- Concerned Officer: Sh. Sandeep Kushwaha EE/HCD-10 9868915016
- Phase-I- Phase-I work is completed.
- Phase-II- The work for Phase-2 is not required.




TODAPUR (802/800)

- District: New Delhi
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- PG letter has been issued dated on 05.08.2026. Phase-I work will be completed by 30-08-2026
- Phase-II- Phase -2 estimate is prepared and under scrutiny. work shall be taken up after completion of Phase I likely to be completed before 30.08.2026. communication letter has been sent to DJB for supply of STP water.

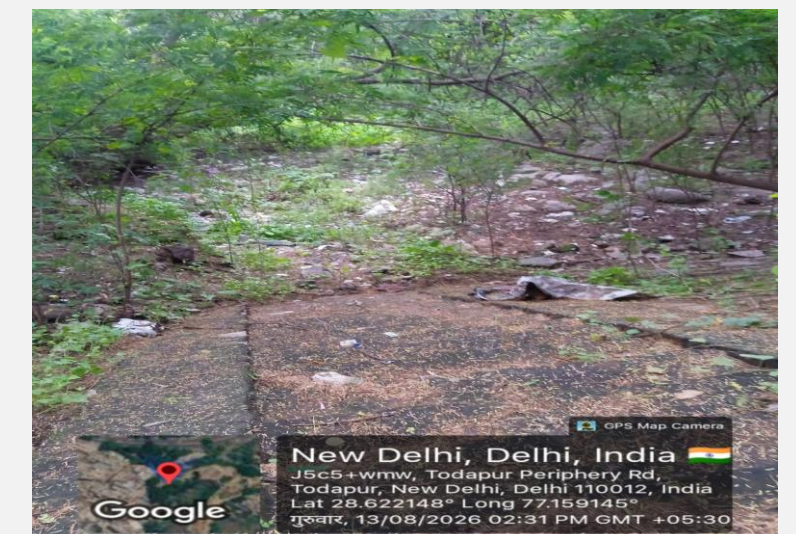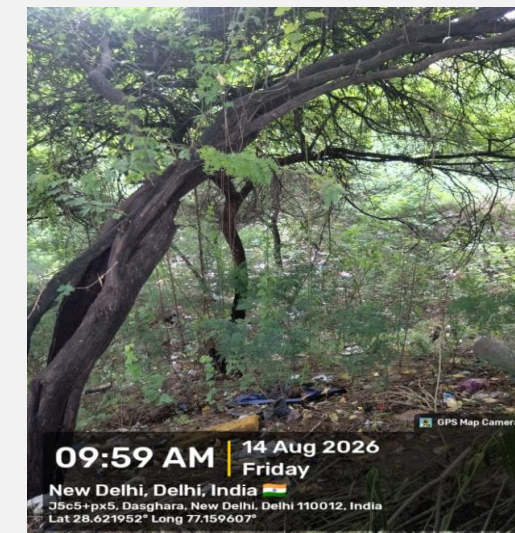



TODAPUR (803/801)

- District: New Delhi
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- PG letter has been issued dated on 05.08.2026. Phase-I work will be completed by 30-08-2026
- Phase-II- Phase -2 estimate is prepared and under scrutiny. Work shall be taken up after completion of Phase I likely to be completed before 30.08.2026. communication letter has been sent to DJB for supply of STP water.

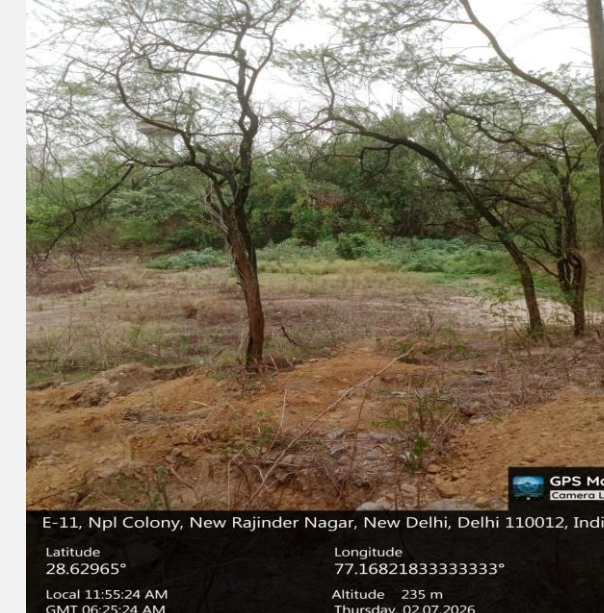



TODAPUR (804/802)

- District: New Delhi
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- PG letter has been issued dated on 05.08.2026. Phase-I work will be completed by 30-08-2026
- Phase-II- Phase -2 estimate is prepared and under scrutiny. Work shall be taken up after completion of Phase I likely to be completed before 30.08.2026. communication letter has been sent to DJB for supply of STP water.

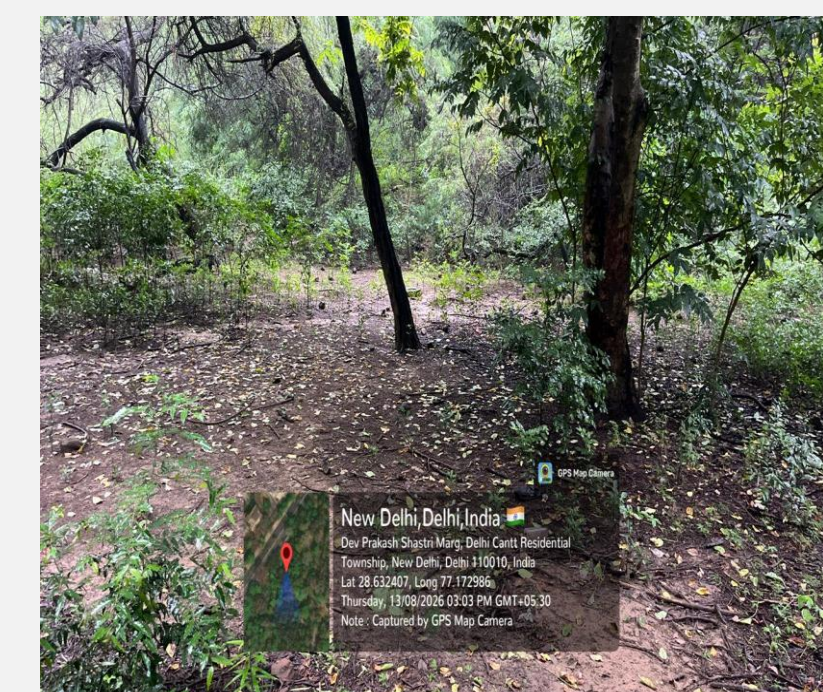

TIHAR LAKE

- District: West
- Concerned Officer: Sh. Rakesh Kumar EE/HCD-8 9958681549
- Phase-I- Works under phase I completed.
- Phase-II- Detailed estimate for Ph-II is being prepared. Estimate shall include repainting of exiting fencing, Installation of spouts for collection of rainwater, repair of red sand stone pathway around lake, installation of informatory boards & signage and other miscellaneous works. communication letter has been sent to DJB for supply of STP water.

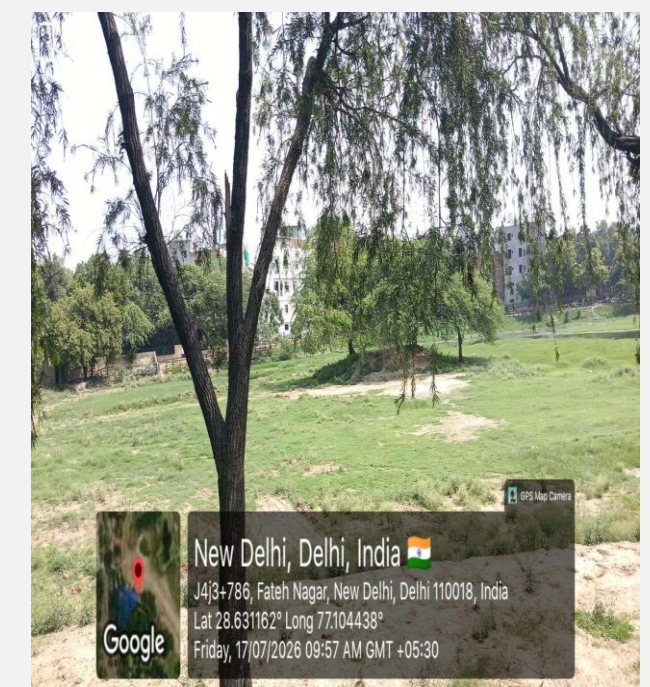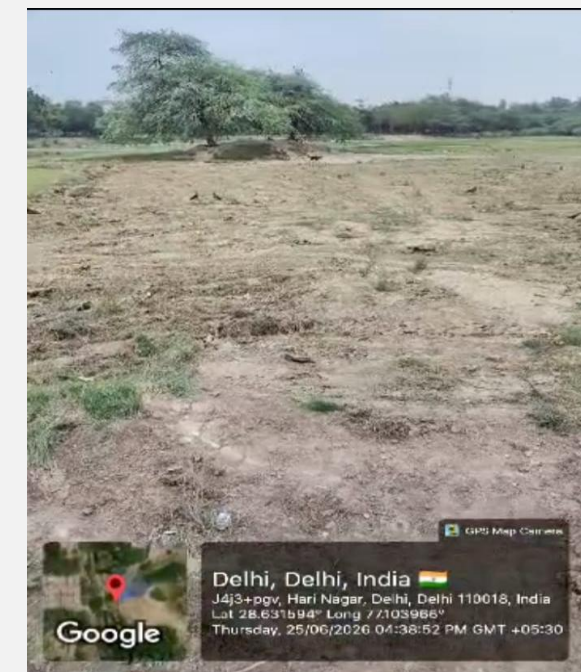

DISTRICT PARK, HARSH VIHAR, PITAMPURA

- District: North West
- Concerned Officer: Sh. Dunni Ram Meena EE/HCD-5 7042737470
- Phase-I- Works under phase I completed.
- Phase-II- The work for Phase-II has been awarded, comprising repair of fencing around the lake, repair of the existing stone pitching and laying of pipelines for channelizing water from the catchment areas into the lake. Works under Phase II will be completed by 31 Dec 2026
- For perennial water supply to maintain the water level in the lake, an estimate has been submitted for A/A & E/S for installation of an STP of 200 KLD capacity. New STP target date 31.05.2027.





DISTRICT PARK AT SECTOR-20, ROHINI (PHASE-3)

- District: North West
- Concerned Officer Sh. Manoj Kumar Mishra EE/HCD-6 8800355584
- Phase-I- Works under Phase- I completed.
- Phase-II- In r/o phase-II it is submitted that necessary infrastructure is available at site except treated water for which necessary coordination is being done with DJB, target date 31.05.2027.



NHP NO. 3 AT SECTOR 23, ROHINI (JHEEL WALA PARK)

- District: North West
- Concerned Officer: Manoj Kumar Mishra EE/HCD-6 8800355584
- Phase-I- Works under Phase- I completed
- .Phase-II- In r/o phase-II it is submitted that necessary infrastructure is available at site.

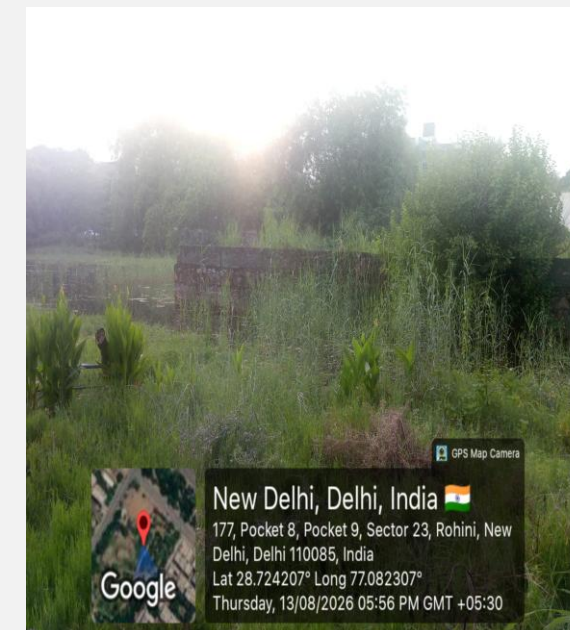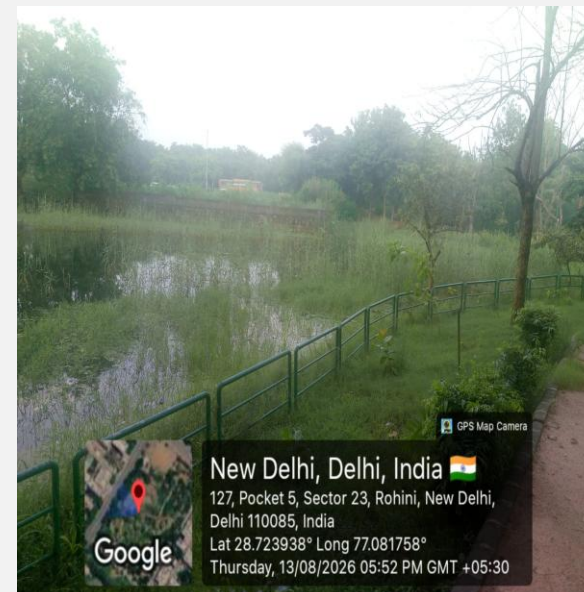



RITHALA F/89 (PARK AND WATER BODY AT RITHALA, SECTOR-5, ROHINI)

- District: North West
- Concerned Officer Sh. Manoj Kumar Mishra EE/HCD-6 8800355584
- Phase-I- Works under phase I completed.
- Phase-II- Works under Phase II , the work of laying the pipeline for collection of rainwater is presently under the tendering process. the work will be completed by 31.12.2026 . necessary correspondence was made by the office of EE/HCD-6 with the concerned offices of DJB seeking permission for extraction of untreated sewage water for installation of High KLD STP. In pursuance thereof, a communication has been received from DJB, wherein permission for extraction of untreated sewage water at Sector-5, Rohini, has been denied.




SUBHASH CAMP BADARPUR

- District: South East
- Concerned Officer: Sh. Saurabh Mishra EE/HCD-2 7054520525
- Phase-I- Restoration of the boundary wall has been completed.
- All works proposed under Phase-I have been completed.
- The waterbody has been properly developed and rejuvenated.
- No desilting is required at present, as the waterbody is in satisfactory condition.
- Phase-II- The civil work proposed under Phase-II have been completed. However, the waterbody is in dry condition.

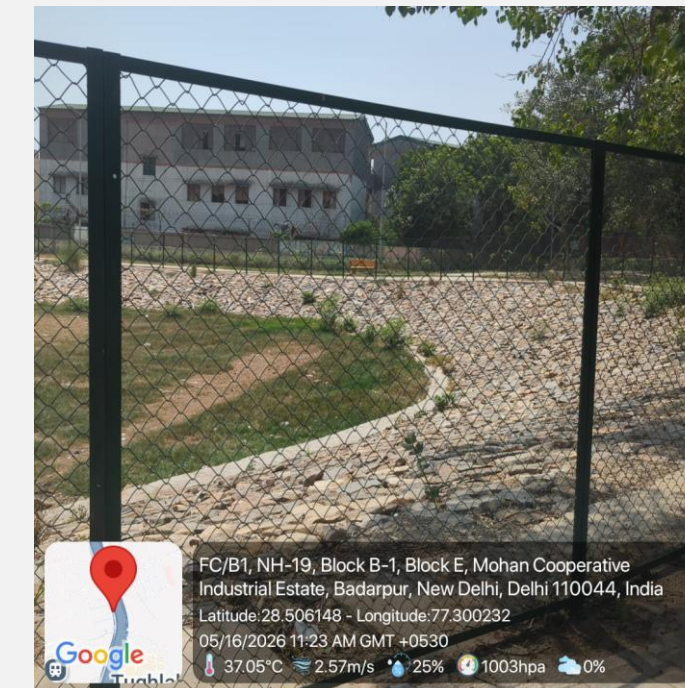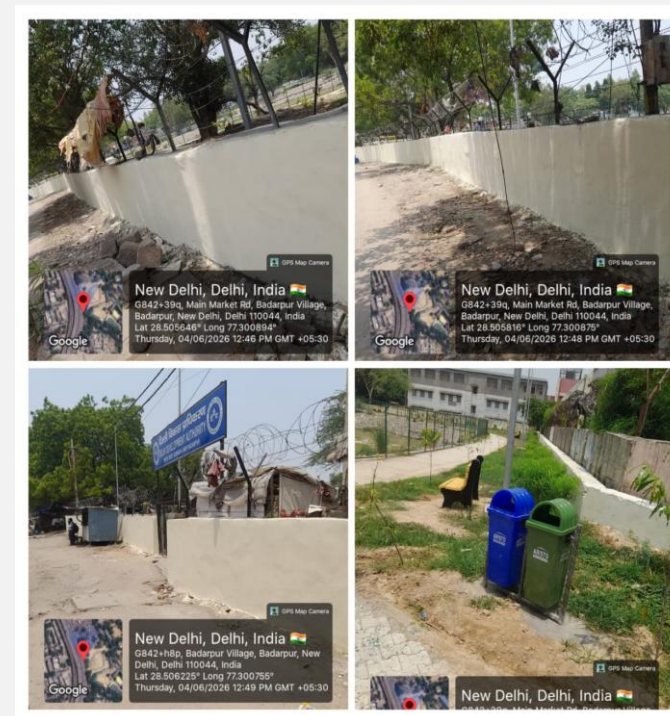



SMRITI VAN NARELA

- District: North
- Concerned Officer Sh. Dunni Ram Meena EE/HCD-5 7042737470
- Phase-I- Works under phase I completed.
- Phase-II- The estimate for Phase-II works, comprising installation of fencing around the lake and laying of pipelines for channelizing water from the catchment areas into the lake, has been submitted for approval and sanction. Works under Phase II will be completed by 31 March 2027.
- Perennial water supply for maintaining the water level in the lake is proposed to be provided by the Delhi Jal Board (DJB). Letters have already been written to DJB in this regard (under 200 parks). Target date 31.05.2027.



AASTHA KUNJPH-I LL ILL (DISTT. PARK, KALKAJI I/C PARK AROUND KALKAJI TEMPLE) GARHI JHARIA MARIA F/66

- District: South East
- Concerned Officer: Sh. Ashutosh Upadhyay EE/HCD-3 9315869127
- Phase-I- Surface excavation, dredging dressing and cleaning of weeds and jungle have been completed.
- Phase-II- The estimate for Phase-II works comprising installation of fencing around the lake, signage boards and laying of pipelines for channelizing water from the catchment areas into the lake and other misc works is under tendering process and Works under Phase II will be completed by 30 April 2027.
- The preliminary estimate for water supply through STP for Phase II has been submitted for sanction of Administrative Approval and Expenditure Sanction (A/A & E/S) by the competent authority. The work shall be completed within 180 days from the date of award of the work. Accordingly, the tentative date of completion of the work envisaged under Phase II is 30.04.2027.

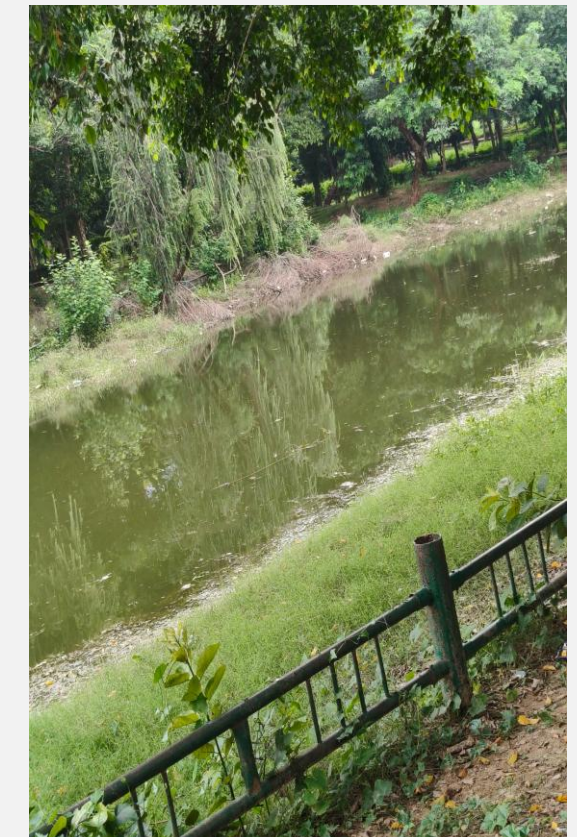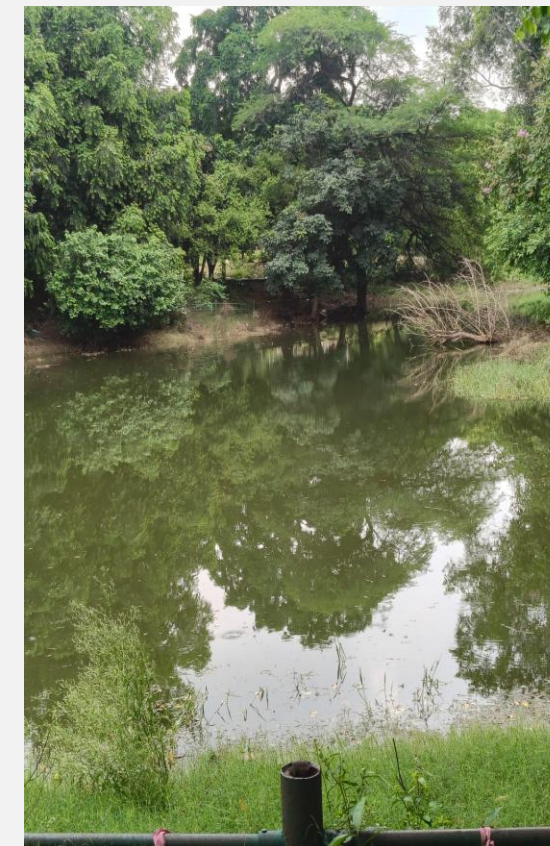

BHALSWA JAHANGIRPURI, BEHIND SANJAY ENCLAVE

- District: North West
- Concerned Officer: Sh. Dunni Ram Meena EE/HCD-5 Mob 7042737470
- Phase-I- Works under phase I completed.
- The preliminary estimate for water supply through STP for Phase II has been submitted for sanction of Administrative Approval and Expenditure Sanction (A/A & E/S) by the competent authority. The work shall be completed within 180 days from the date of award of the work. Accordingly, the tentative date of completion of the work envisaged under Phase II is 30.04.2027.

